



SAN DIEGO
INTERNATIONAL
AIRPORT

Capital Improvement Program Update

Capital Improvement Program Oversight
Committee

January 22, 2013

Presented by: Iraj Ghaemi, Director, Facilities Development

Refurbish Concessions Support Infrastructure

Total Project Budget: \$17.3 million


Construction Schedule:

Construction Start: July 2012

Construction Completion: November 2013

Refurbish Concessions Support Infrastructure

Overall Concession Plan

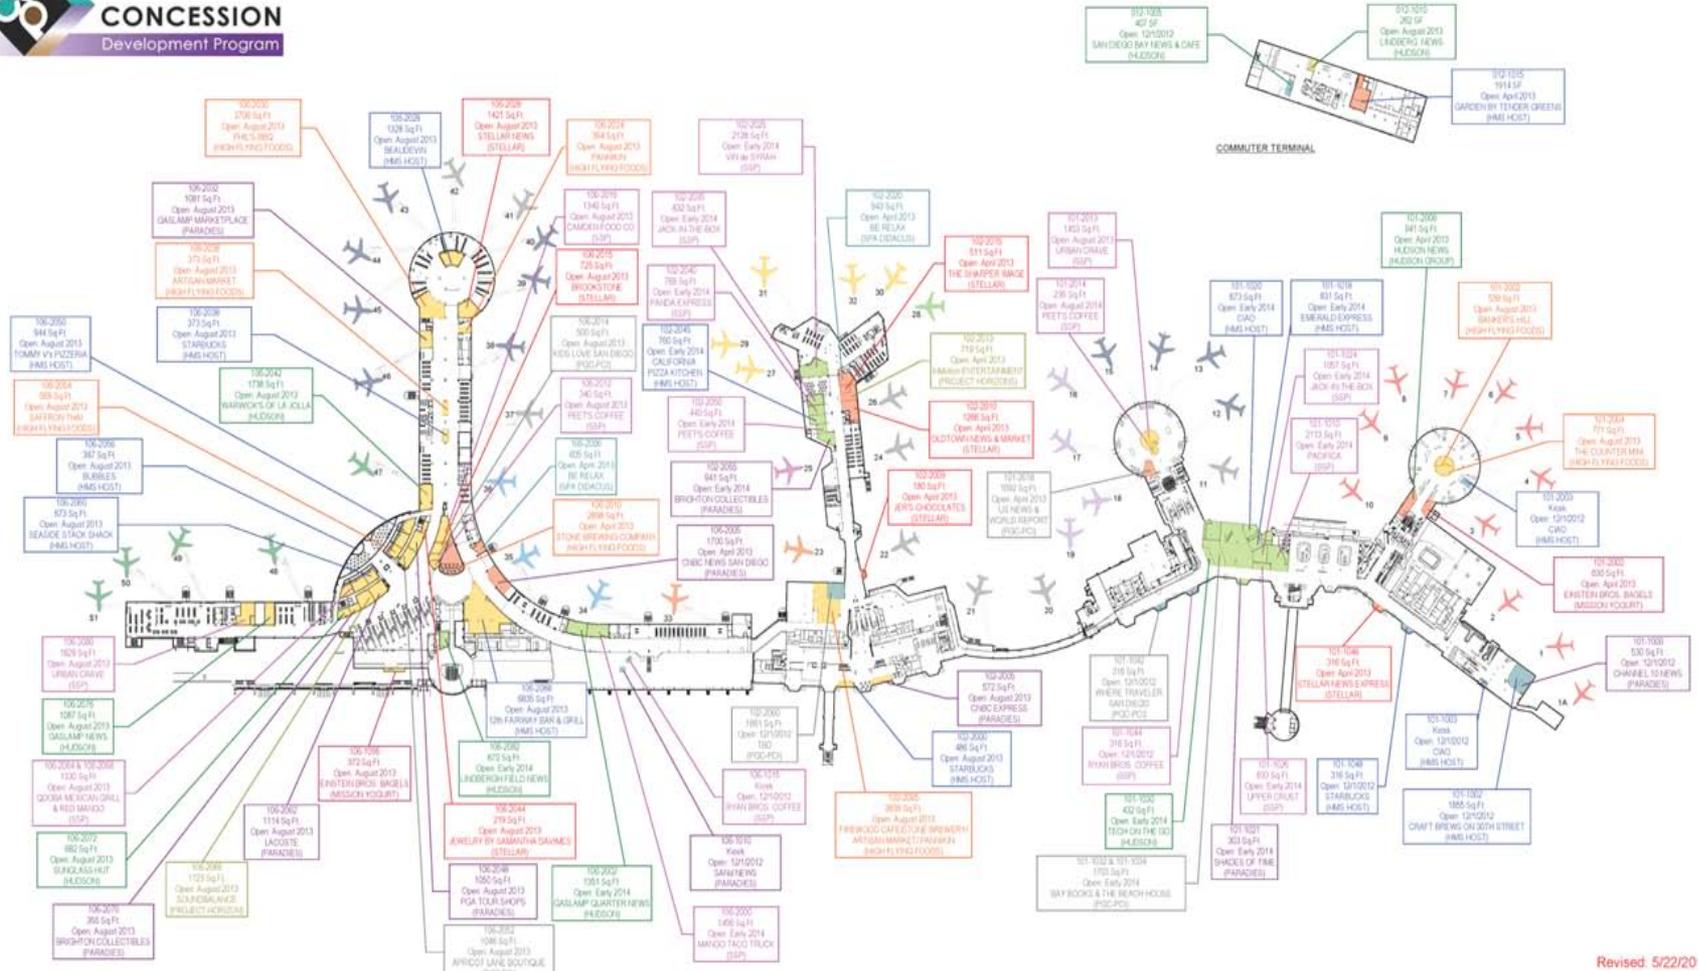


Revised: 5/22/2012

Refurbish Concessions Support Infrastructure

Terminal 2 West & Commuter Terminal

REFURBISH CONCESSIONS SUPPORT INFRASTRUCTURE

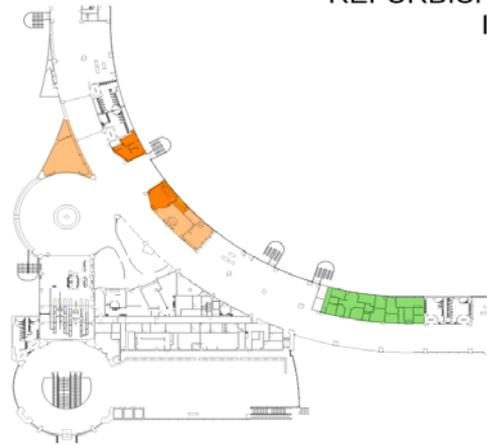


EXISTING - TERMINAL 2 WEST, LEVEL 2




EXISTING - COMMUTER TERMINAL, LEVEL 1

LEGEND EXISTING

FOOD AND BEVERAGE	
RETAIL	
OFFICE CIRCULATION	
FIRST PHASE (COMPLETED OCT. 2012)	

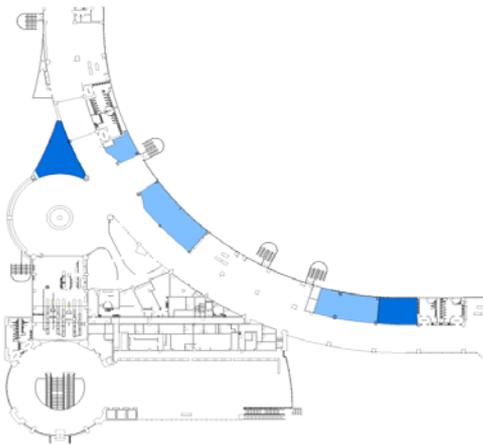

NEW - TERMINAL 2 WEST, LEVEL 2




NEW - COMMUTER TERMINAL, LEVEL 1

LEGEND - NEW

FOOD AND BEVERAGE	
RETAIL	
IMPROVED CIRCULATION	
FIRST PHASE (COMPLETED OCT. 2012)	

Refurbish Concessions Support Infrastructure Terminal 1

REFURBISH CONCESSIONS SUPPORT INFRASTRUCTURE

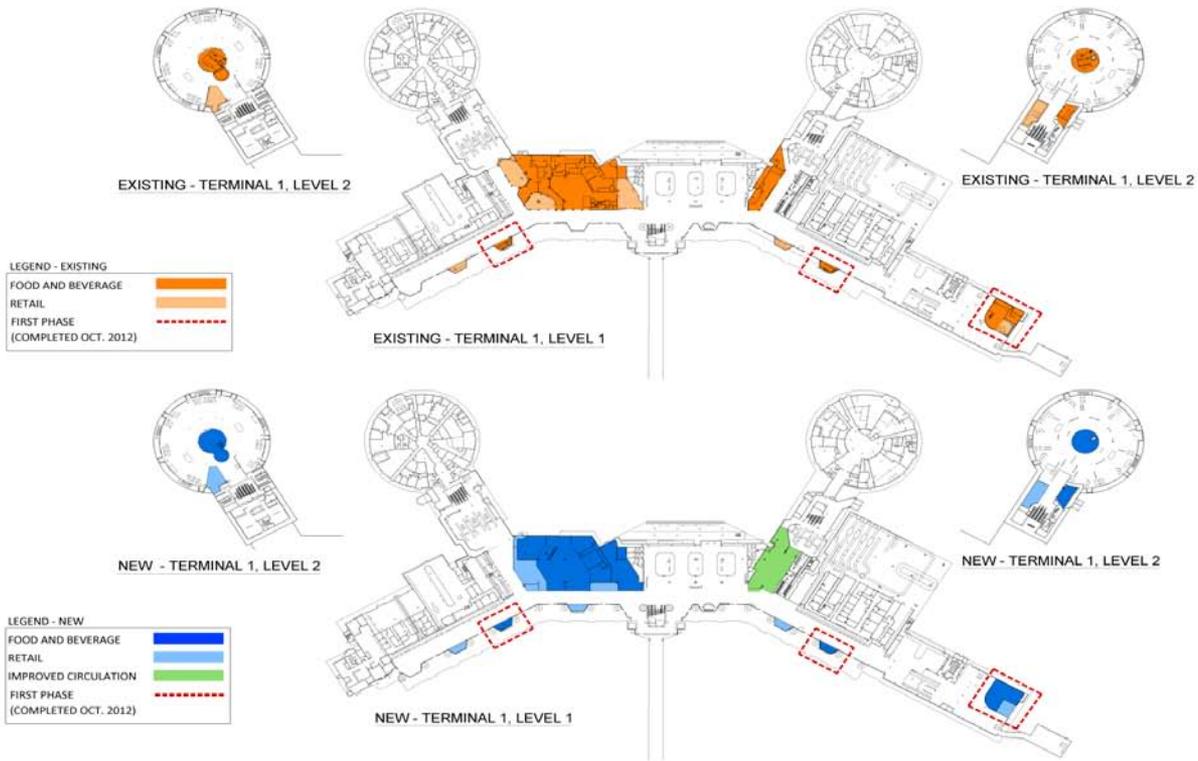

Refurbish Concessions Support Infrastructure

Construction Progress Pictures



Refurbish Concessions Support Infrastructure

Construction progress pictures



Refurbish Concessions Support Infrastructure

Rendering of Future Terminal 1 Food Court

FINISHES	
	WALNUT WOOD CAP
	RUSTICATED MOSAIC TILE
	MARBLE INSET PLANK
	PROPOSED TERRAZZO
	GYP BOARD SOFFIT
	PORCELAIN TILE
	WALNUT WOOD SIGN BAND
	LINEAR WHITE GLASS



FOOD COURT ENTRY



FOOD COURT PYLON SIGN



VIEW FROM BAGGAGE CLAIM



APPROACH FROM BAGGAGE CLAIM




CORRIDOR ELEVATION

Refurbish Concessions Support Infrastructure

Rendering of Future Terminal 1 Food Court




VIEW FROM TICKETING

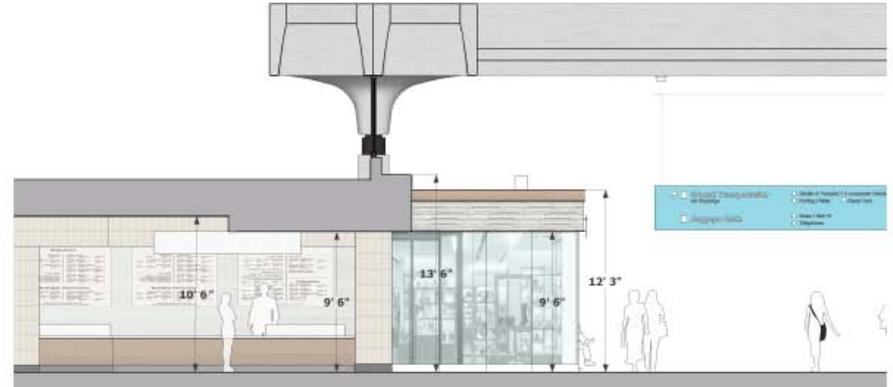


SECTION CUT AT FOOD COURT ENTRY



PROPOSED TERRAZZO

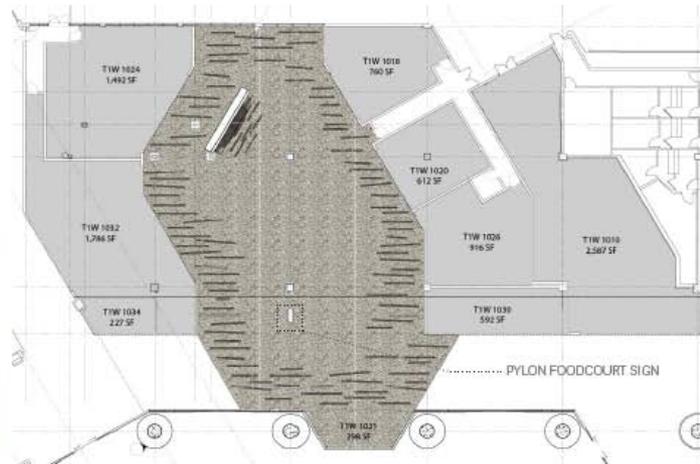

FINISH FLOOR PLAN

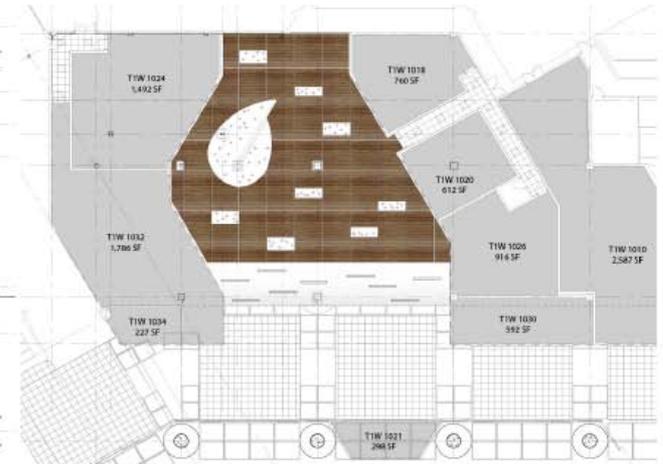

REFLECTED CEILING PLAN

Expand Terminal 2 East Facility

Total Project Budget: \$52 million

Construction Schedule:

Construction Start: February 2012


Construction Completion: October 2013

Expand Terminal 2 East Facility




Expand Terminal 2 East Facility

Existing Facility

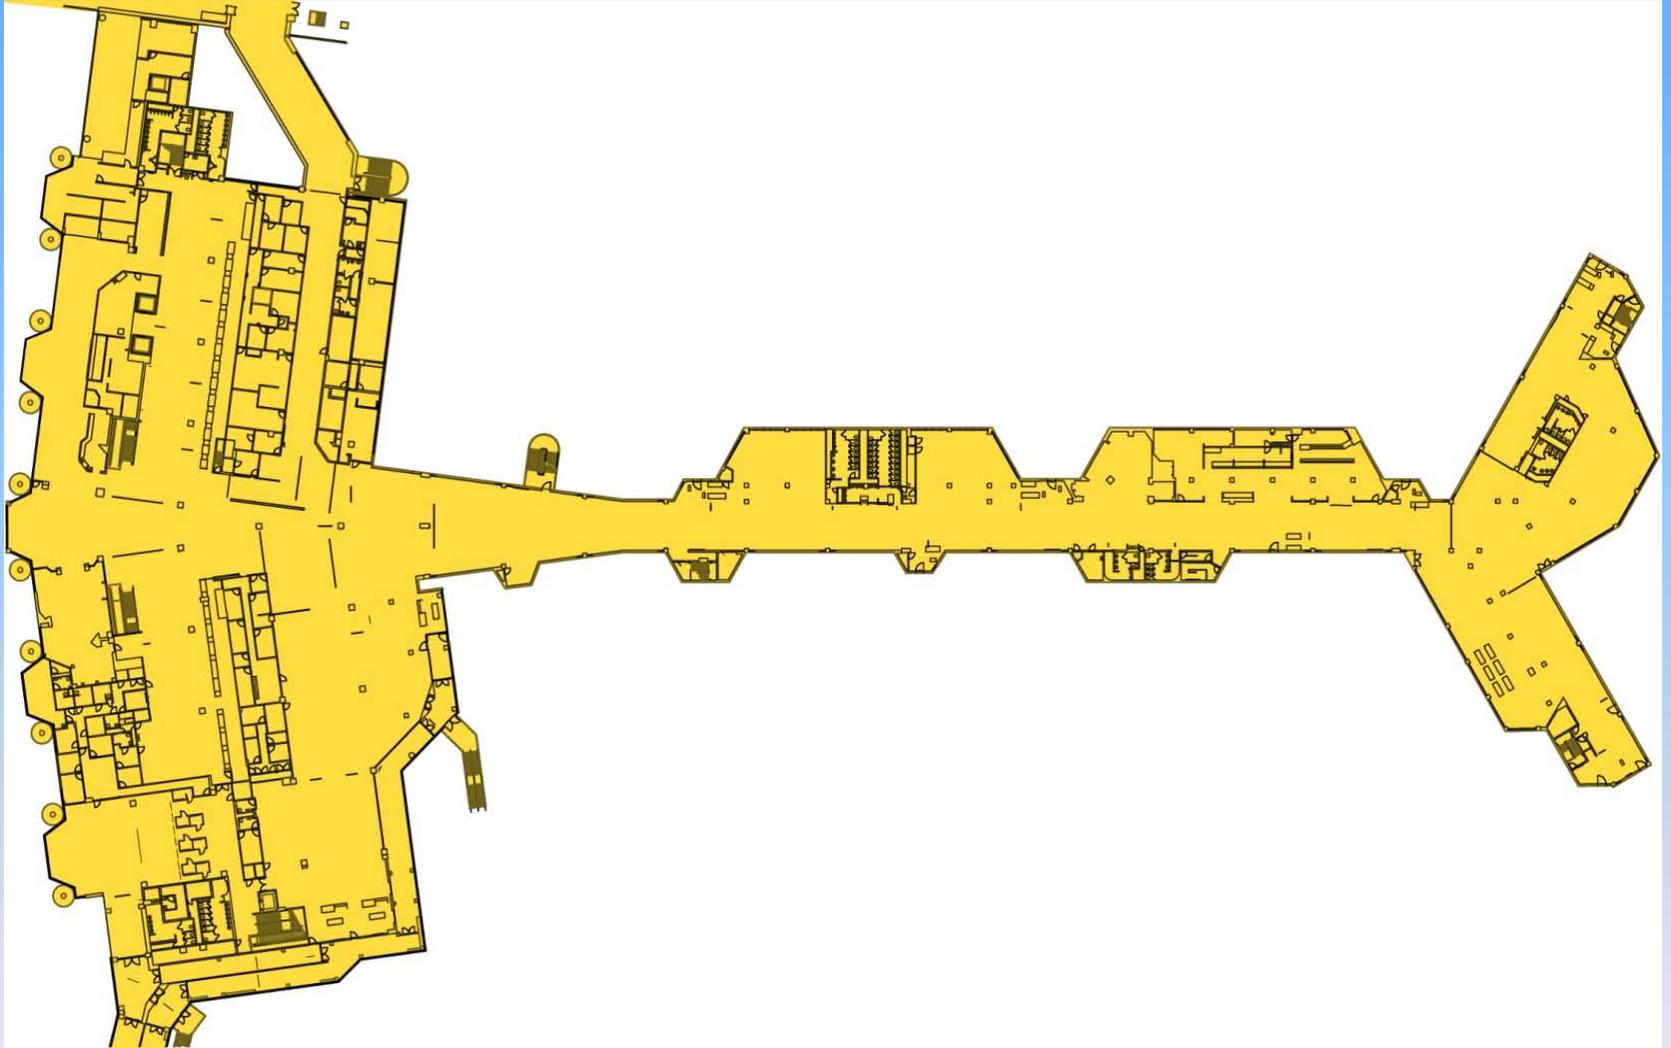


Expand Terminal 2 East Facility

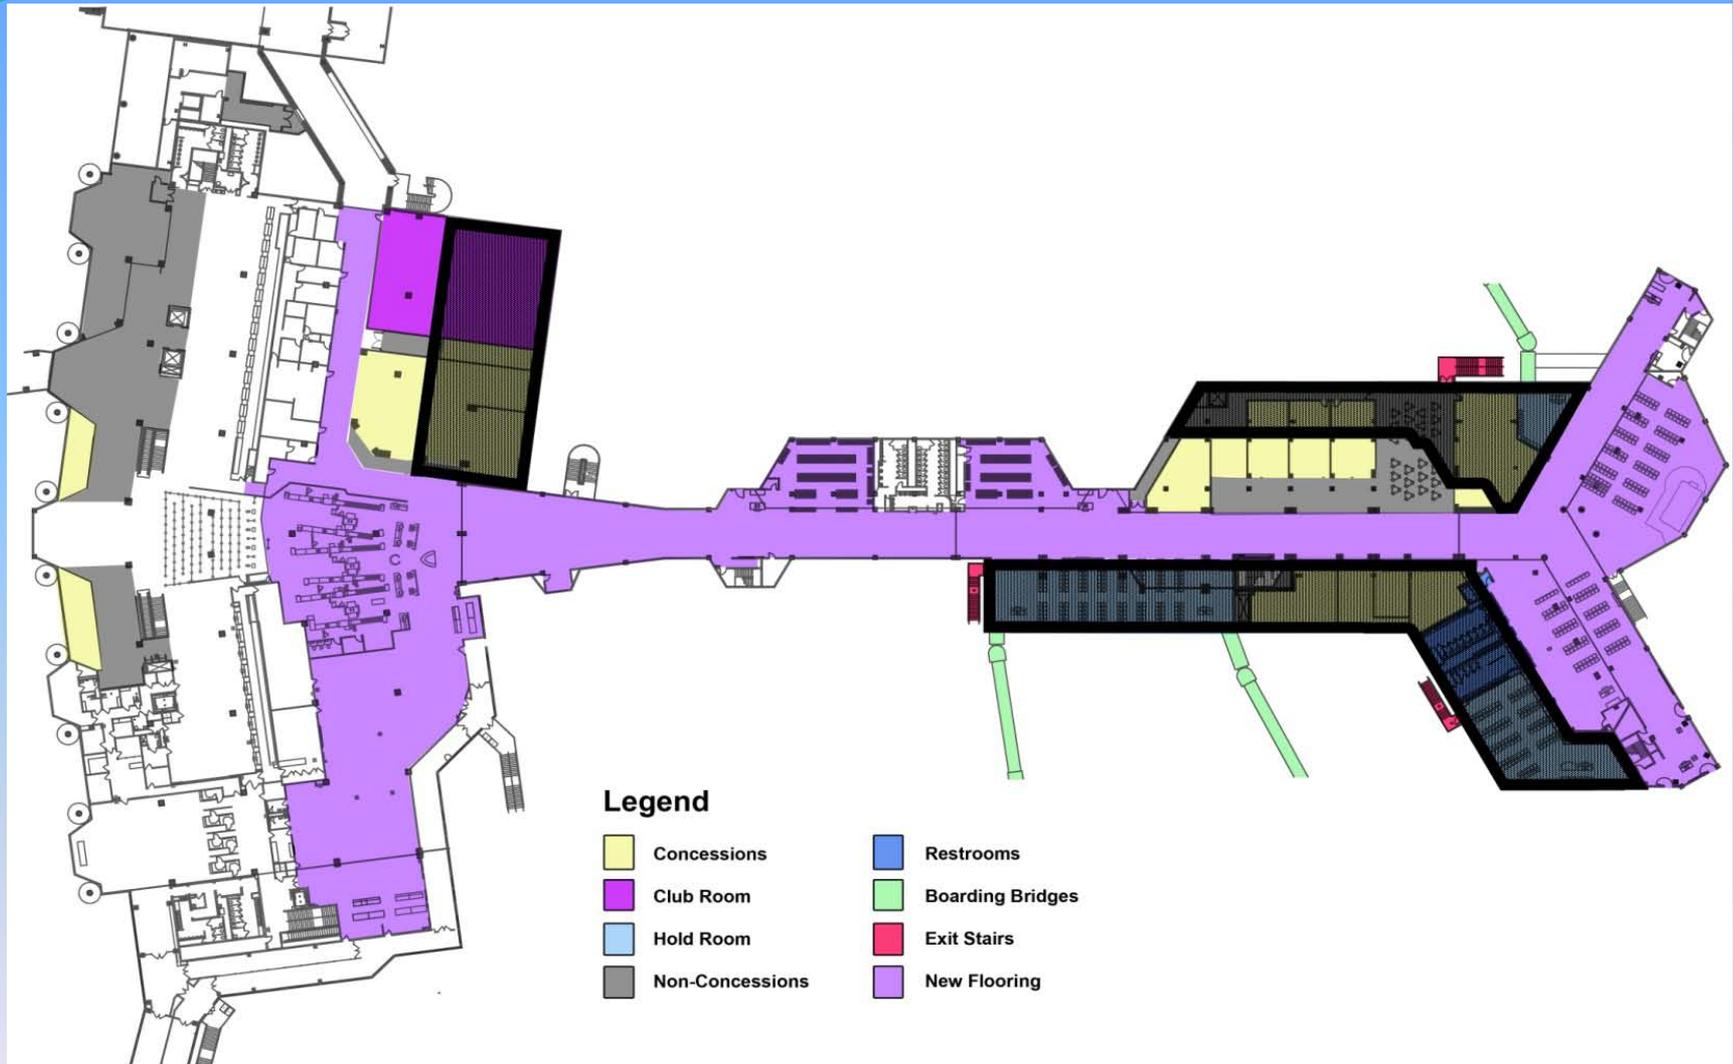


Expanded Terminal 2 East Facility

Terminal Building (South Package) - Post Security Work

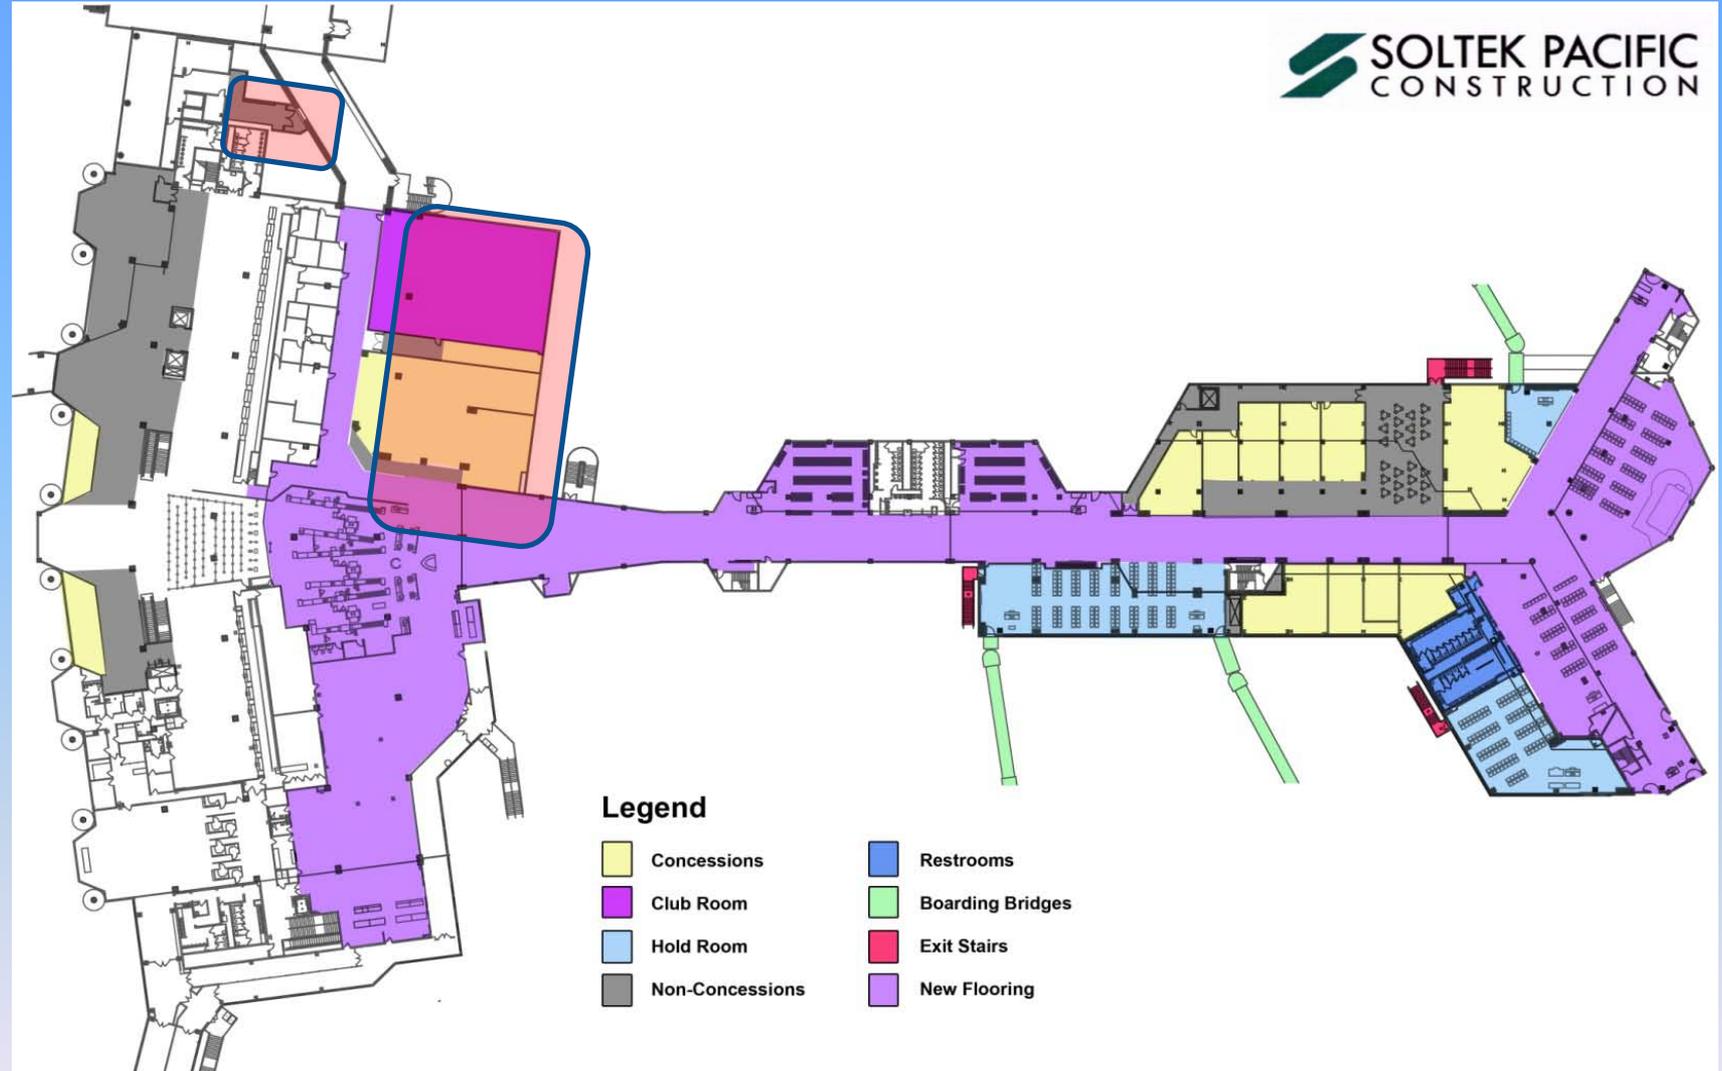

Start: 02/07/2012 Completion: 05/01/2013


Terminal Building (South Package) - Pre Security Work

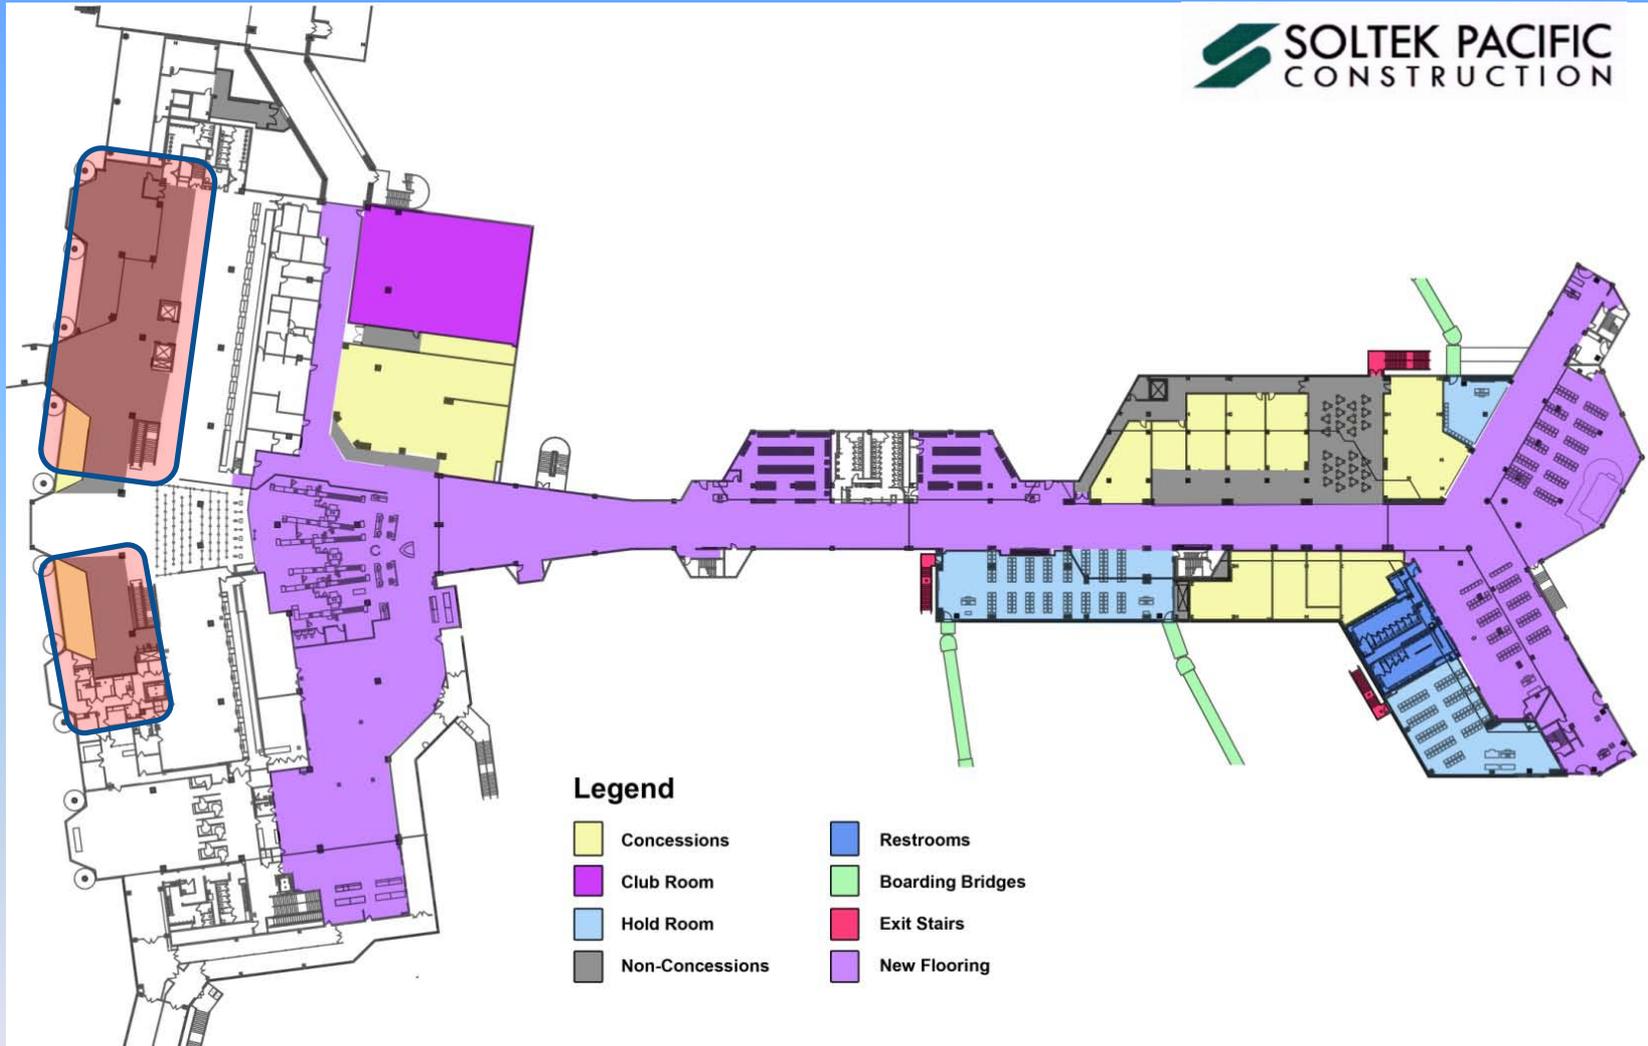

Start: 01/14/2013 Completion: 06/15/2013

Gates 24 - Gate 28 (East Package)


Phase 1 Work

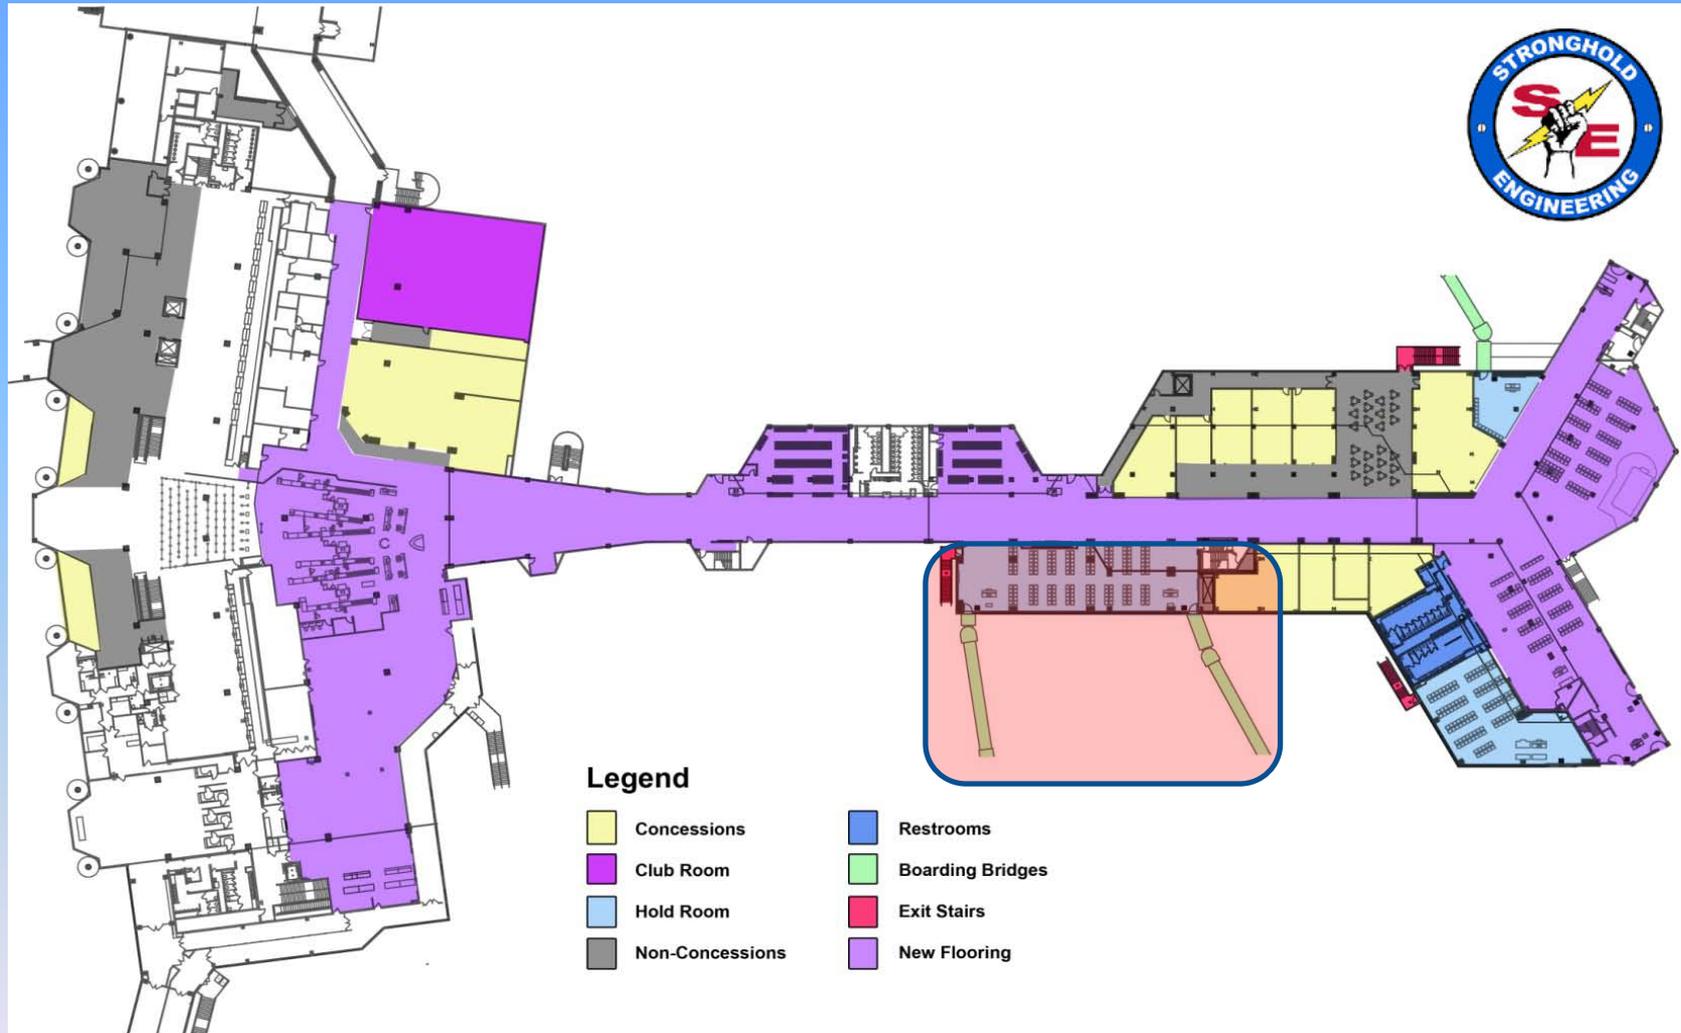

Start: 03/02/2012 Completed: 11/15/2012


Gates 24 - Gate 28 (East Package)

Phase 2 and 3 Work

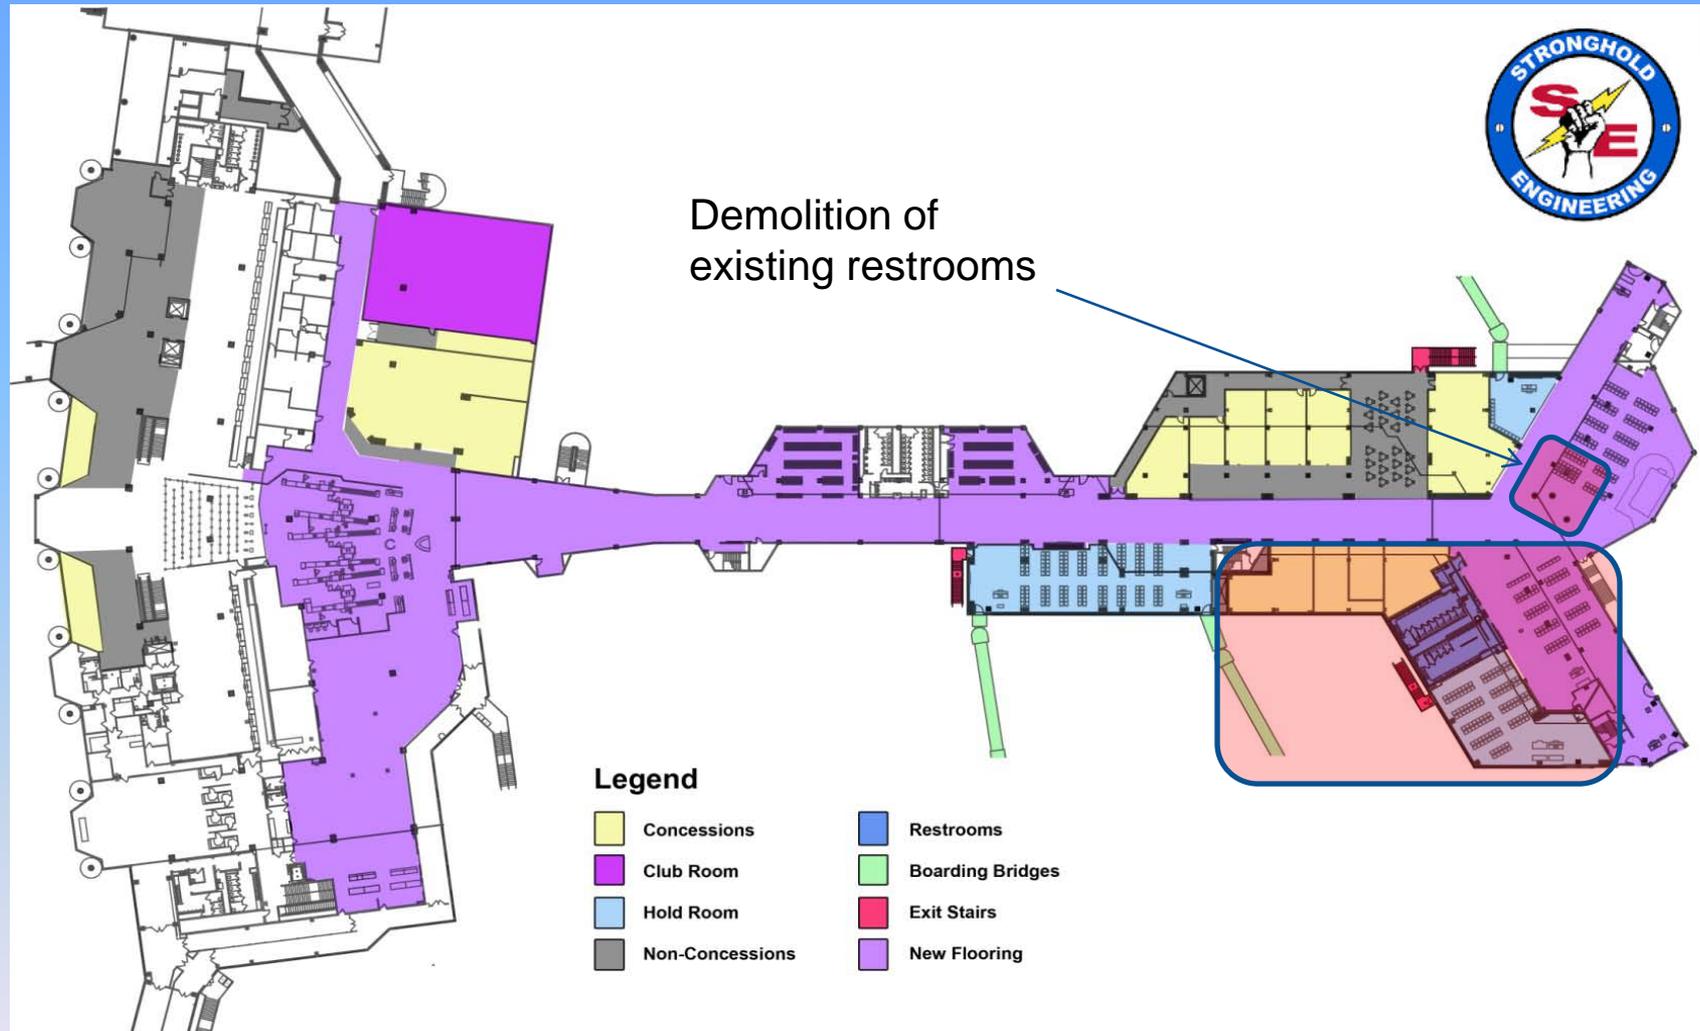

Start: 11/01/2012 Completion: 06/30/2013

Gates 25 - Gate 27 (West Package)

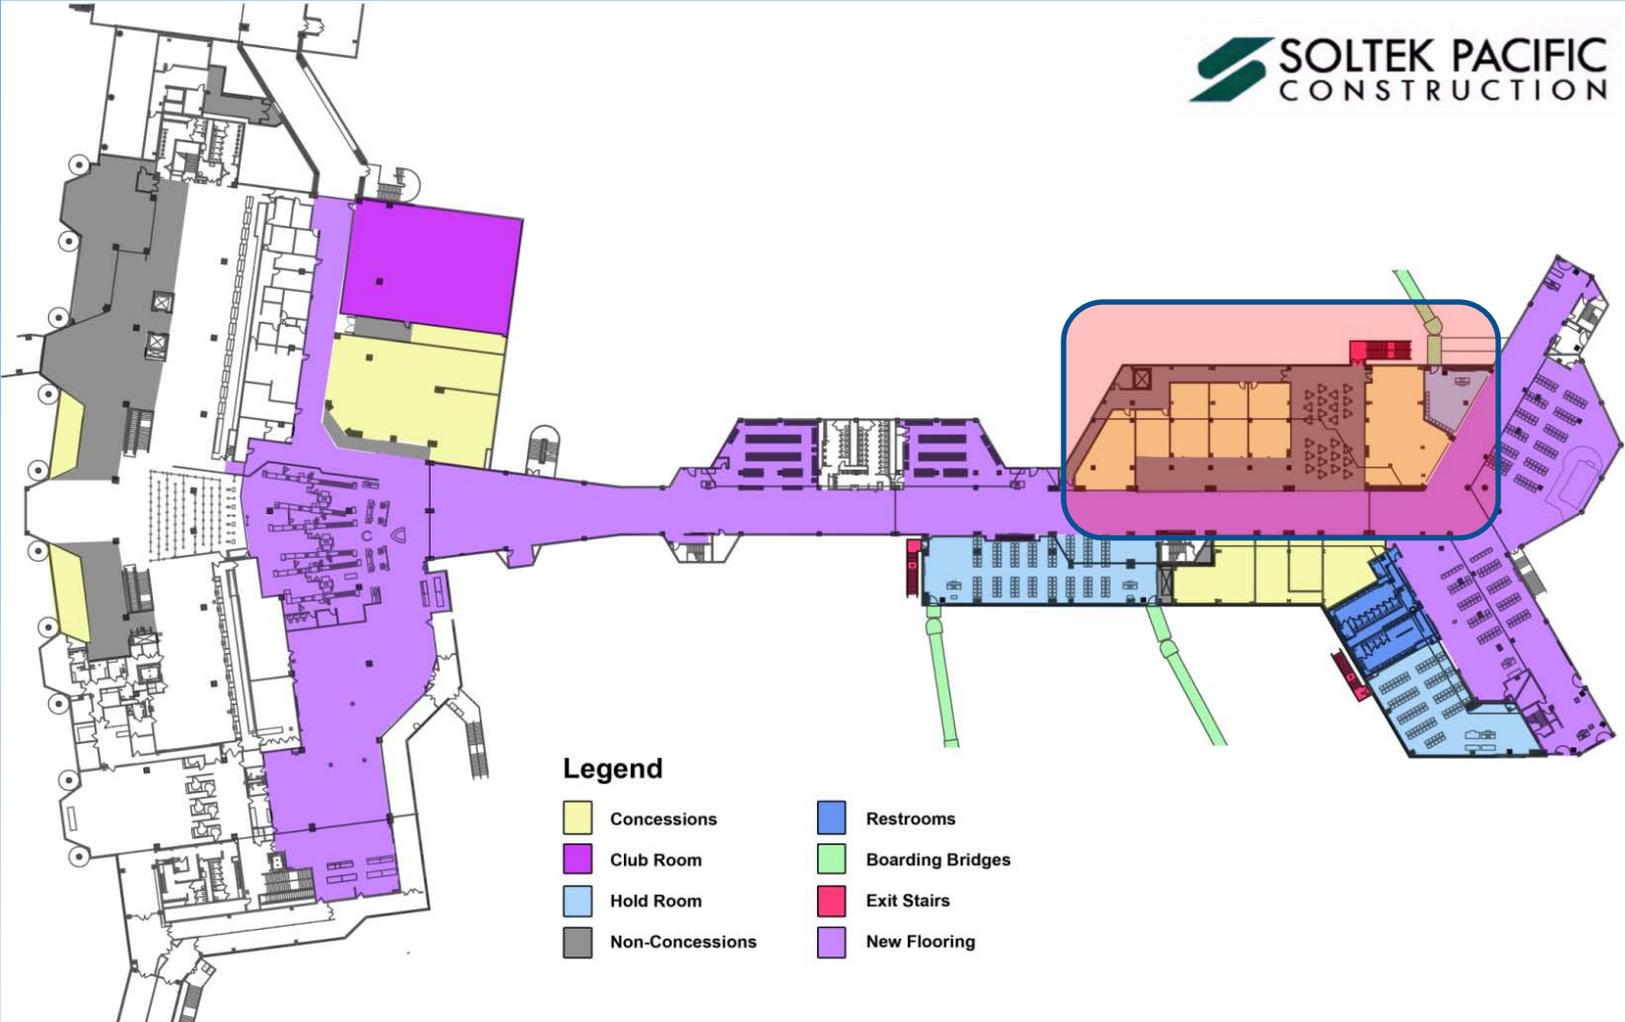

Start: 01/28/2013 Completion: 01/15/2014

Expand Terminal 2 East Facility

Construction Progress Pictures



Expand Terminal 2 East Facility

Construction Progress Pictures




Expand Terminal 2 East Facility

Construction Progress Pictures



Expand Terminal 2 East Facility

Construction Progress Pictures

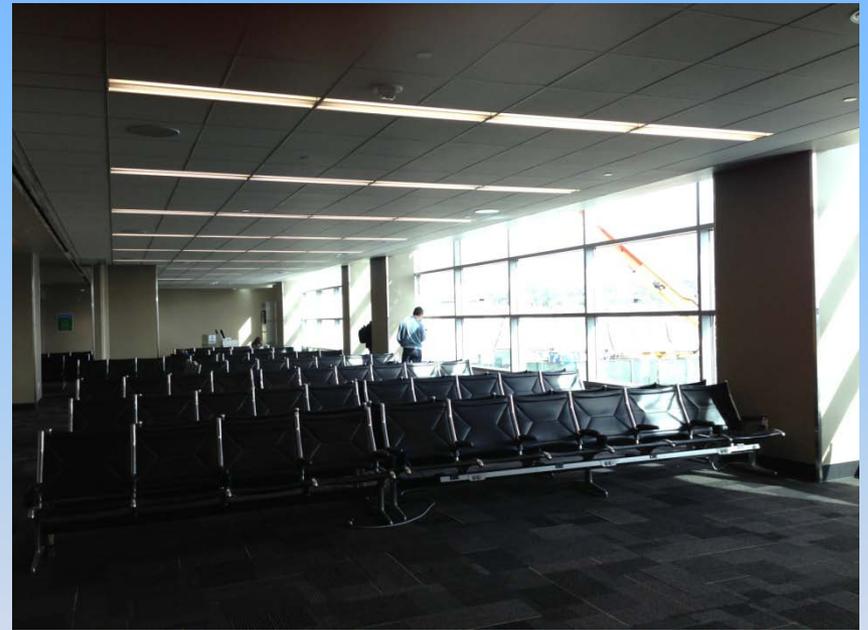

Questions

???
