

# TDP Committee Meeting

Item #2

## Green Build Progress Report

July 10, 2012





# Agenda

- **Contract 1 – Airside & Terminal**
  - **Current Aerial Views**
  - **Progress Photos**
  - **LEED Update**
- **Contract 2 – Landside**
  - **Current Aerial Views**
  - **Progress Photos**
  - **LEED Update**
- **Key Milestones**
- **Construction Status**
- **Budget Status**
- **GMP Contingency Utilization**








San Diego International Airport

# The Green Build

*Moving Forward. Soaring Higher.*




SAN.ORG



San Diego International Airport

# The Green Build

*Moving Forward. Soaring Higher.*



SAN.ORG








Building Skin Completion Target – September 2012










# Baggage Screening Area




**Testing starts September 2012**



A photograph of a large, industrial-looking interior space, likely a baggage handling facility. The area is filled with blue metal structures, possibly conveyor belts or sorting equipment. The ceiling is high and features a complex grid of lights and structural elements. The floor is a light-colored, polished surface. The overall atmosphere is one of a busy, functional environment.

**Checked Bag  
Reconciliation Area**


06/25/2012



# Terrazzo Installation







# Terrazzo Installation





# Terrazzo Installation







- LEED (Leadership in Energy & Environmental Design)
- The Green Build is utilizing LEED NCv2.2 as the certification standard. (Version 3 just released.)
- LEED NCv2.2 - Total of 69 potential points available and 4 levels




Certified: 26 – 32 pts.

Silver: 33 – 38 pts.

Gold: 39 – 48 pts.

Platinum: 49 + pts.



## Airfield/Terminal (Contract 1)

Tracking a possible  
37 – Yes; 9 – Maybe

Design Submitted on 6/15/12

Submitted - 26

Approved - NA

Rejected – NA

\* Have not received comments from USGBC on  
design submittal

Green Building Council Point System

**Silver: 33 to 38**

**Gold: 39 to 51**






**Contract 2 Landside**



San Diego International Airport

# The Green Build

Moving Forward. Soaring Higher.



## Elevated Departures Roadway May 30, 2012



Central Utility Plant  
Online July 2012



San Diego International Airport

# The Green Build

Moving Forward. Soaring Higher.



## Bridges H & K, Frames 3 & 4

May 30, 2012





San Diego International Airport

# The Green Build

*Moving Forward. Soaring Higher.*



# USO/PMO

May 30, 2012


















## Landside (Contract 2)

Tracking a possible  
39 – Yes; 8 – Maybe

### Design Submitted on 4/30/12

Submitted - 27

Approved - 14

Rejected – 0


\*USGBC provided comments on 6/1/12 and  
architect has responded; currently awaiting  
USGBC response

### Green Building Council Point System


**Silver: 33 to 38**


**Gold: 39 to 51**





# C1 Key Milestones

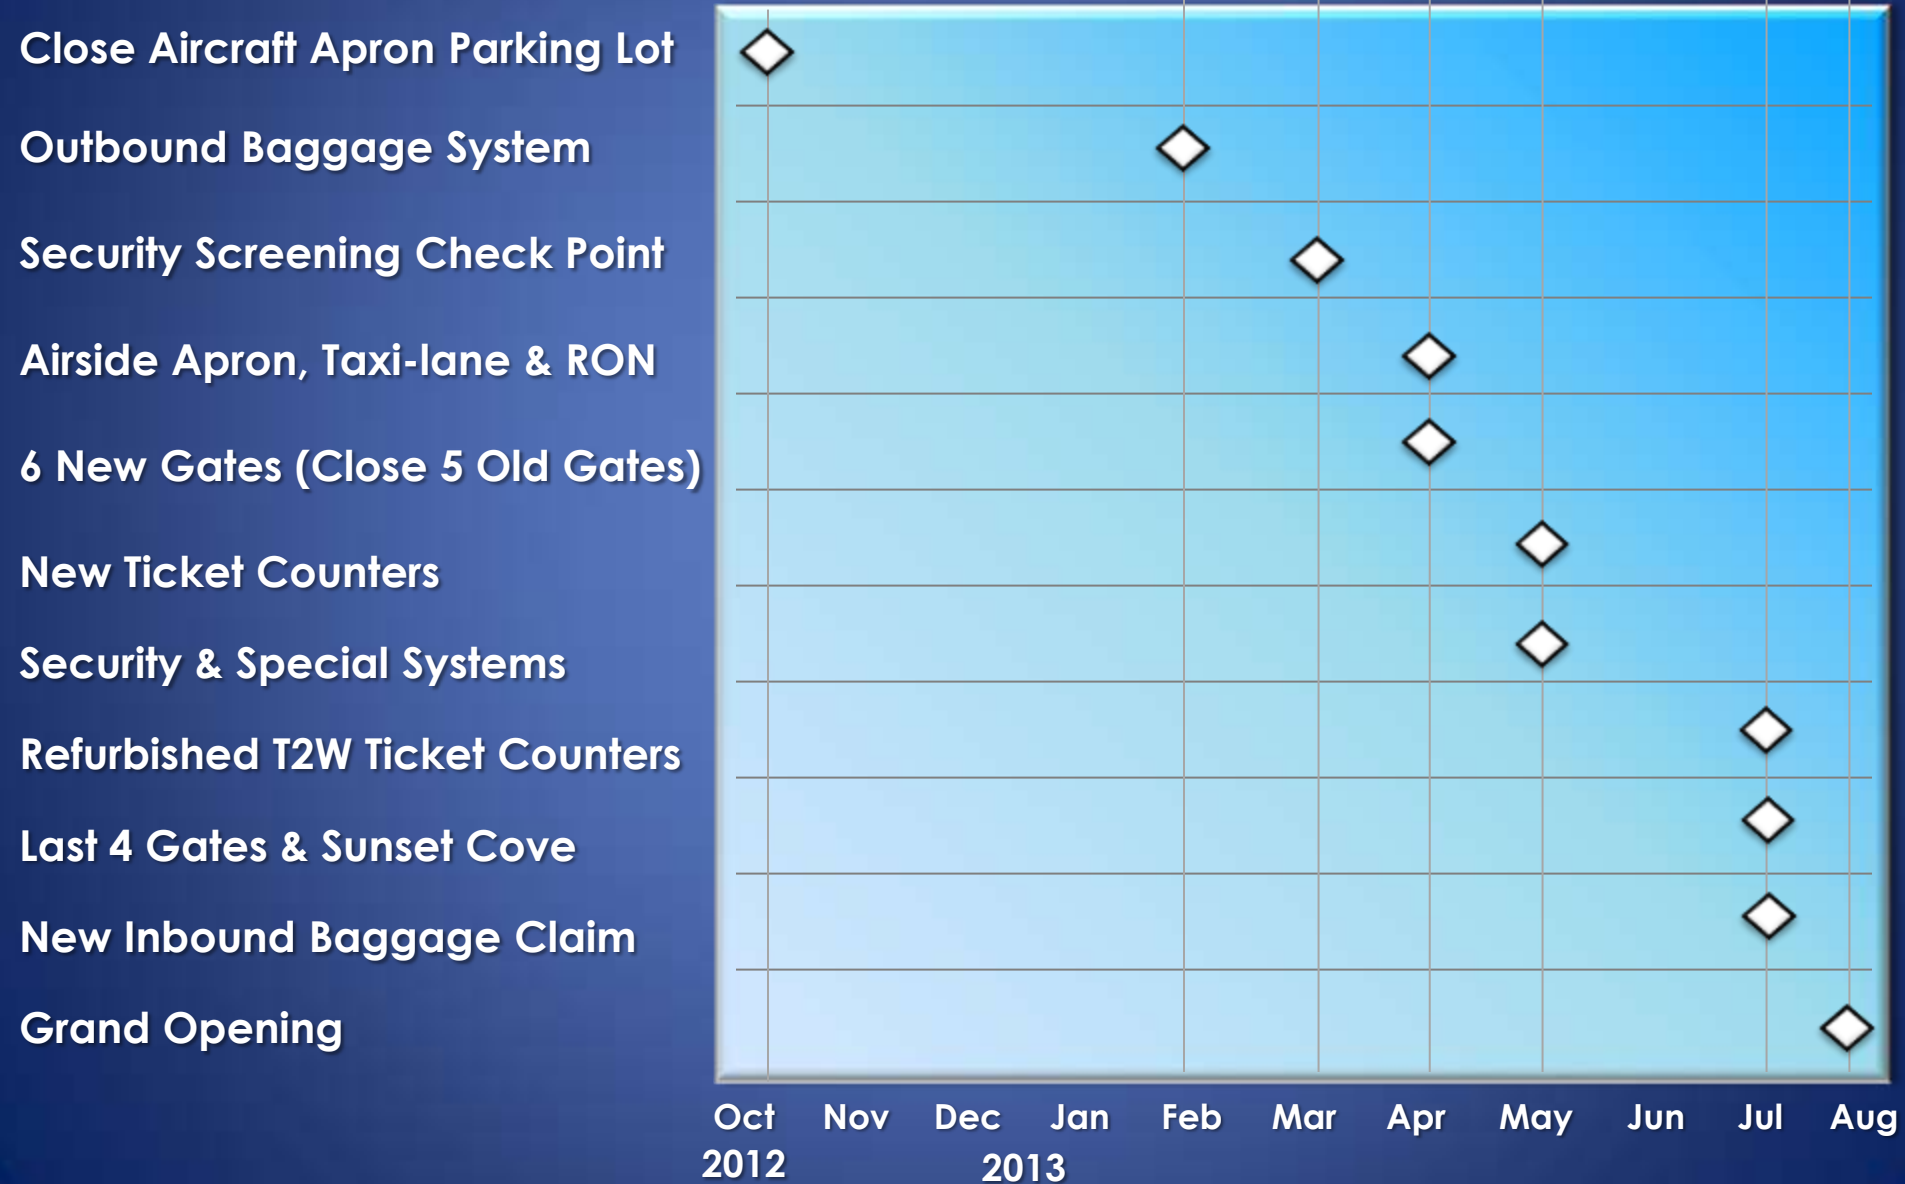



# C2 Key Milestones

Open East Transit Center

Open 700 Parking Spaces

Occupy PMO

Open Additional  
210 Parking Spaces

Open Entire Parking Lot


Open Entire Transit Center

Occupy USO

Open East Pavilion

Open West Pavilion


Open EDR

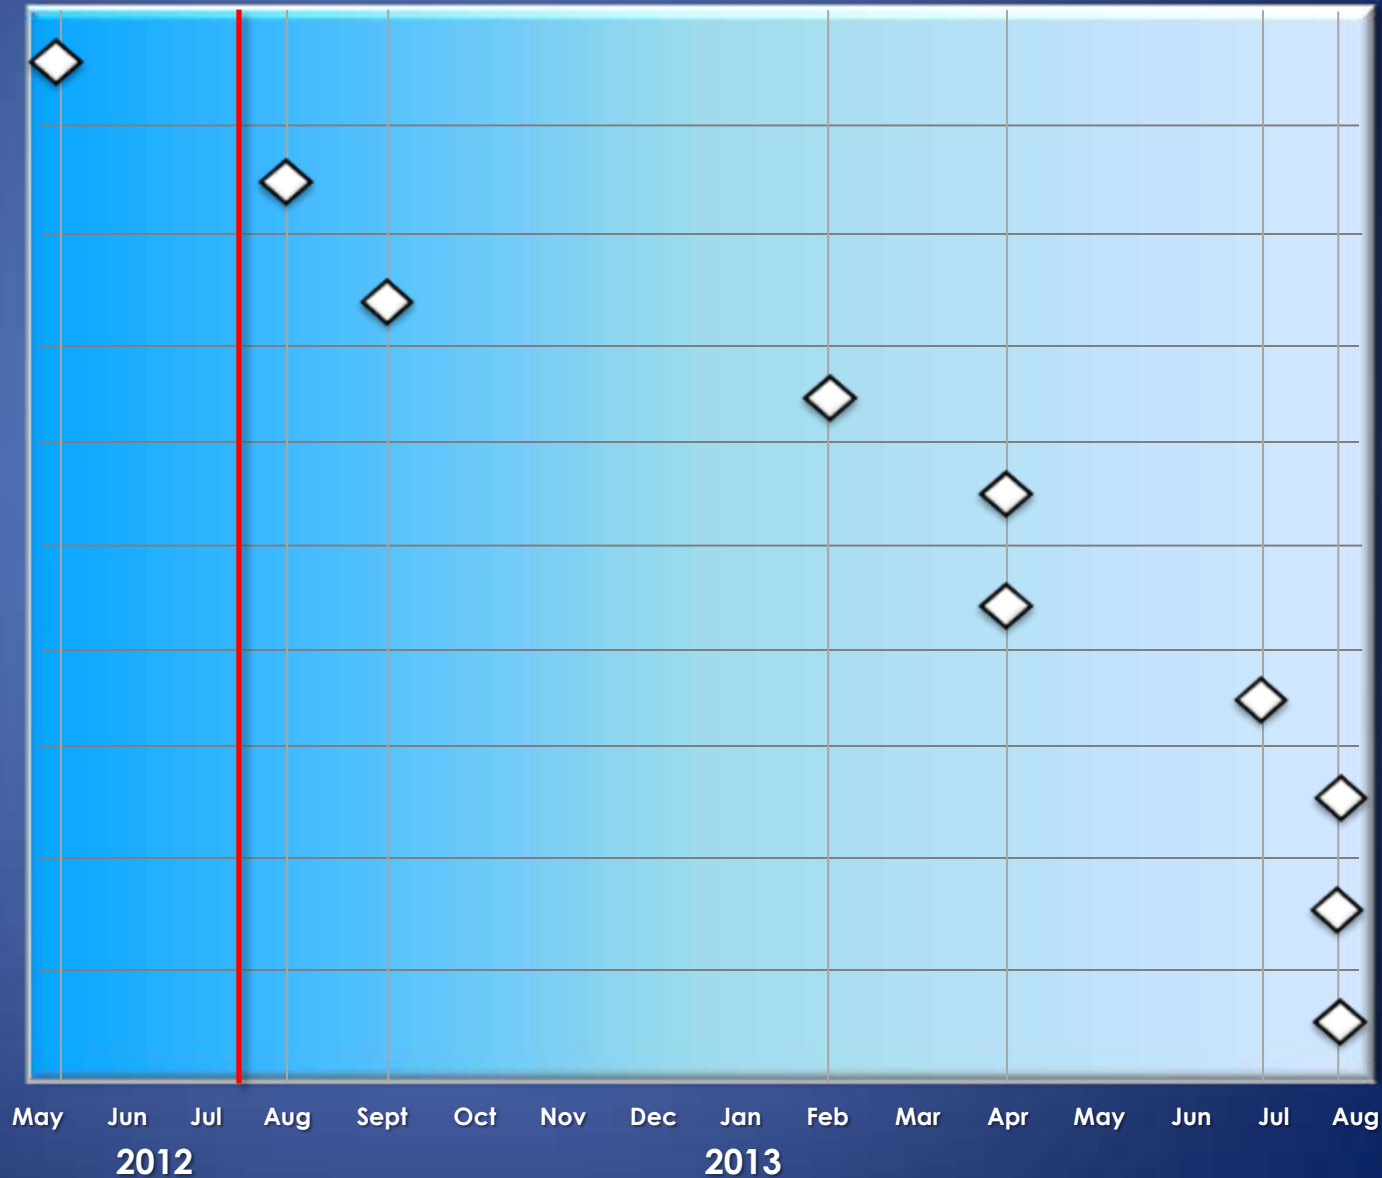







Data as of May 31, 2012

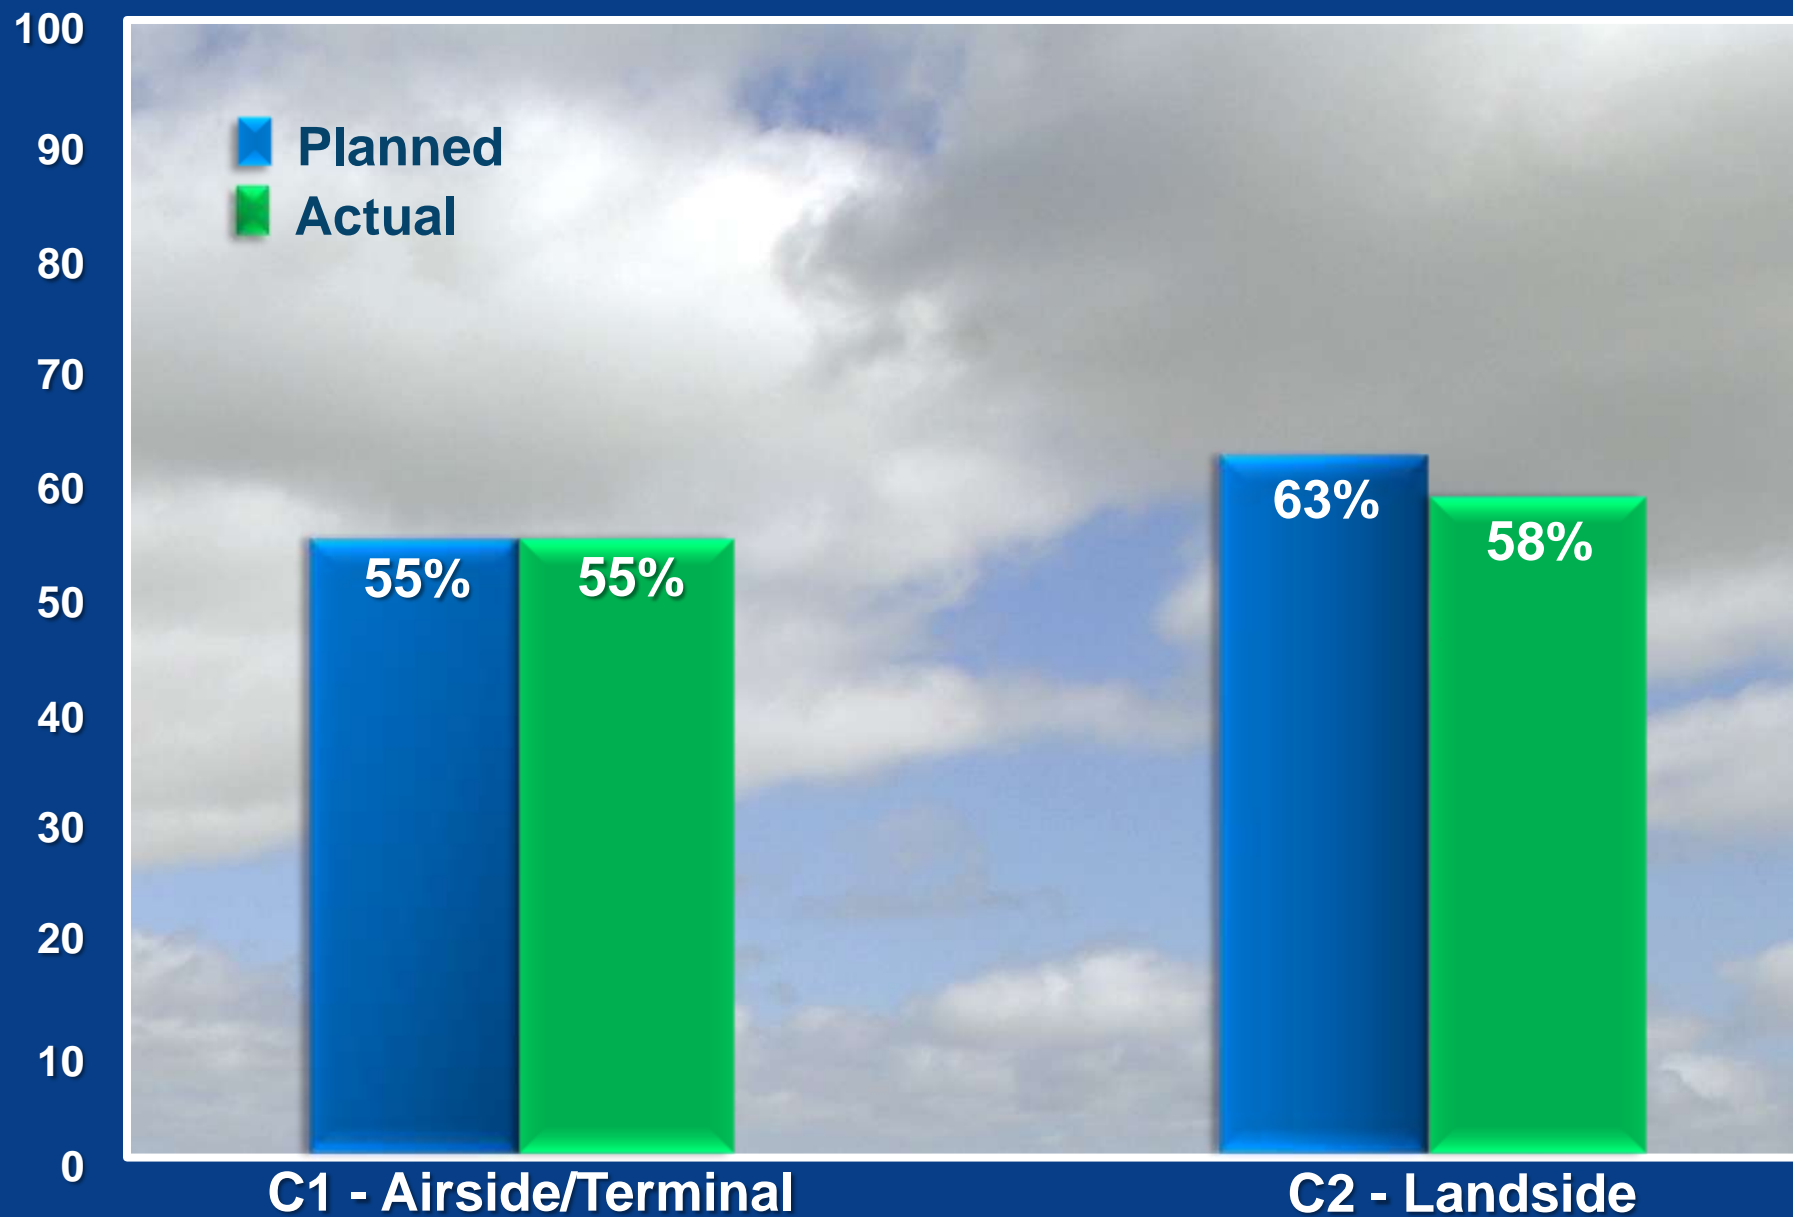




# Budget Status

Data as of May 31, 2012

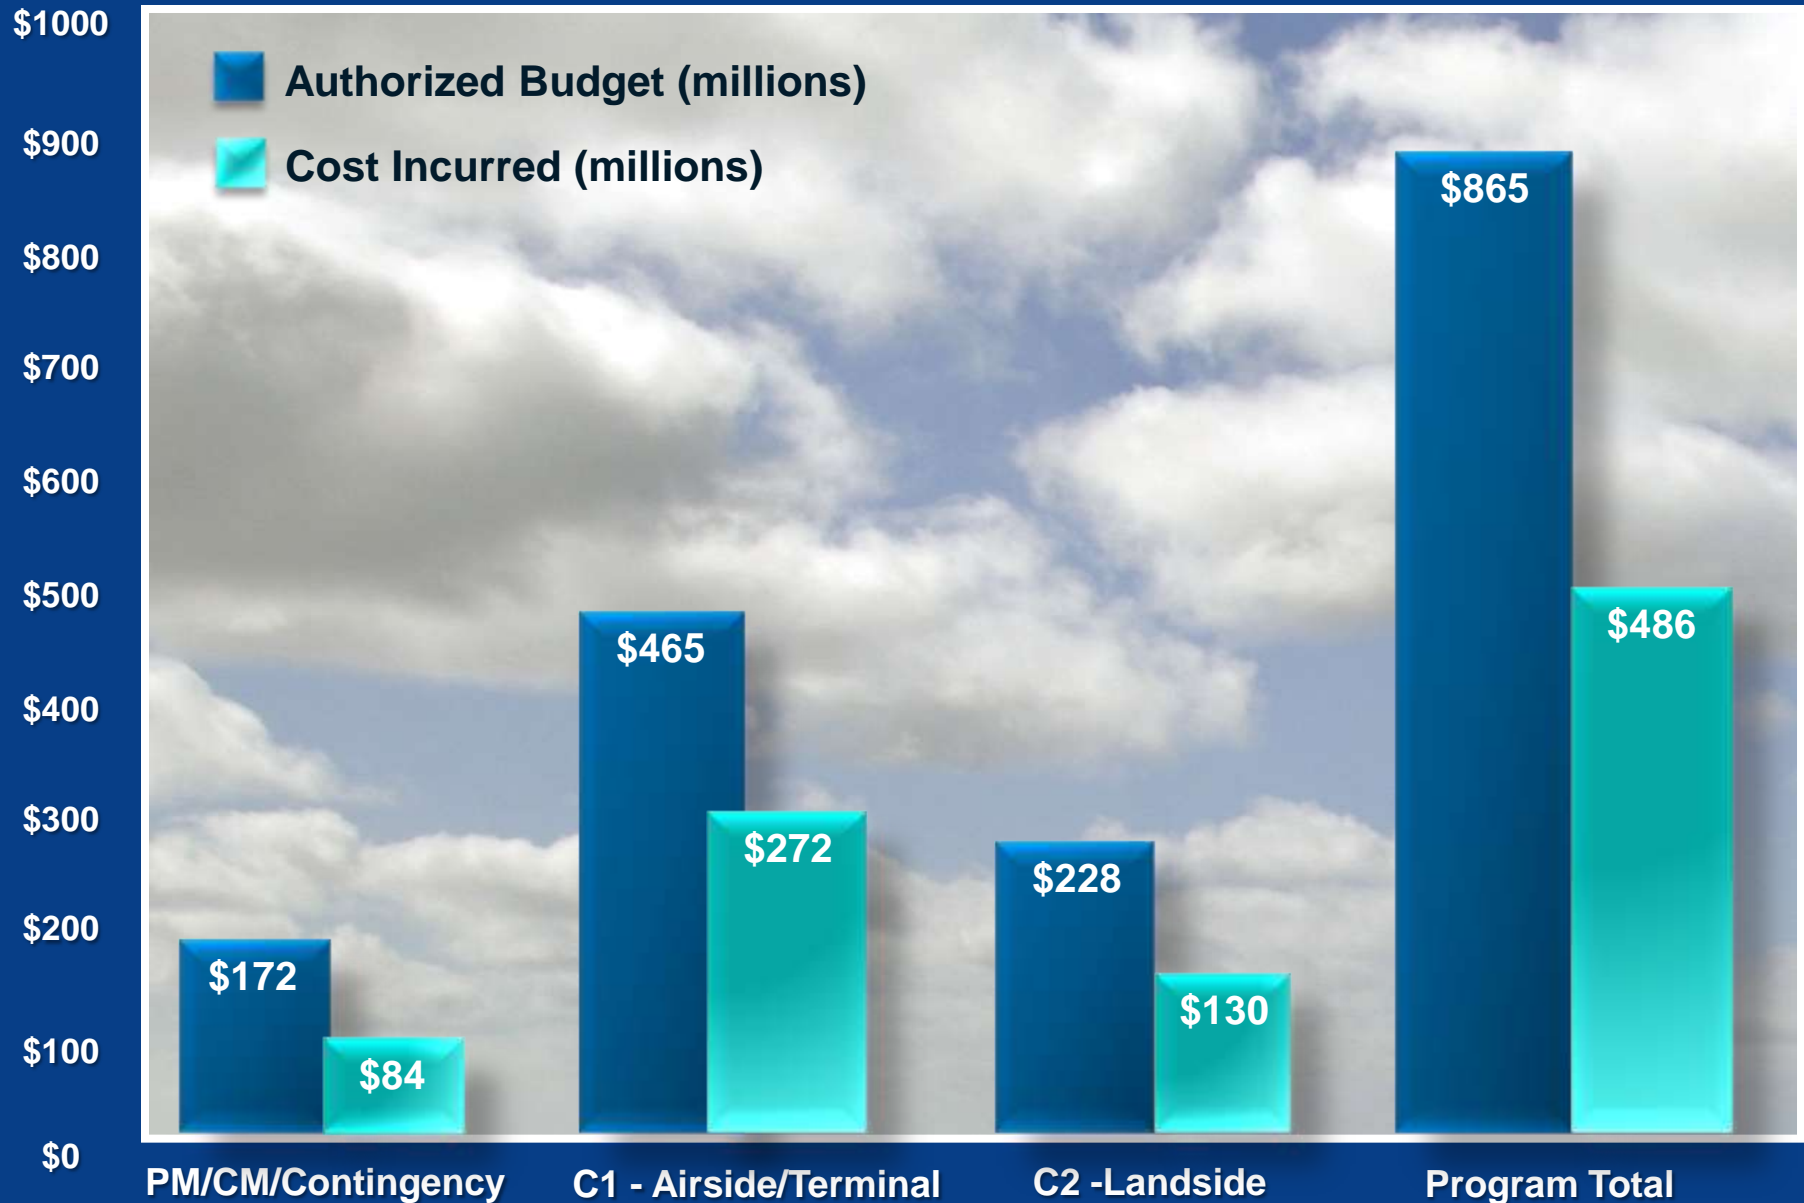






# Contingency Utilization

Data as of May 31, 2012

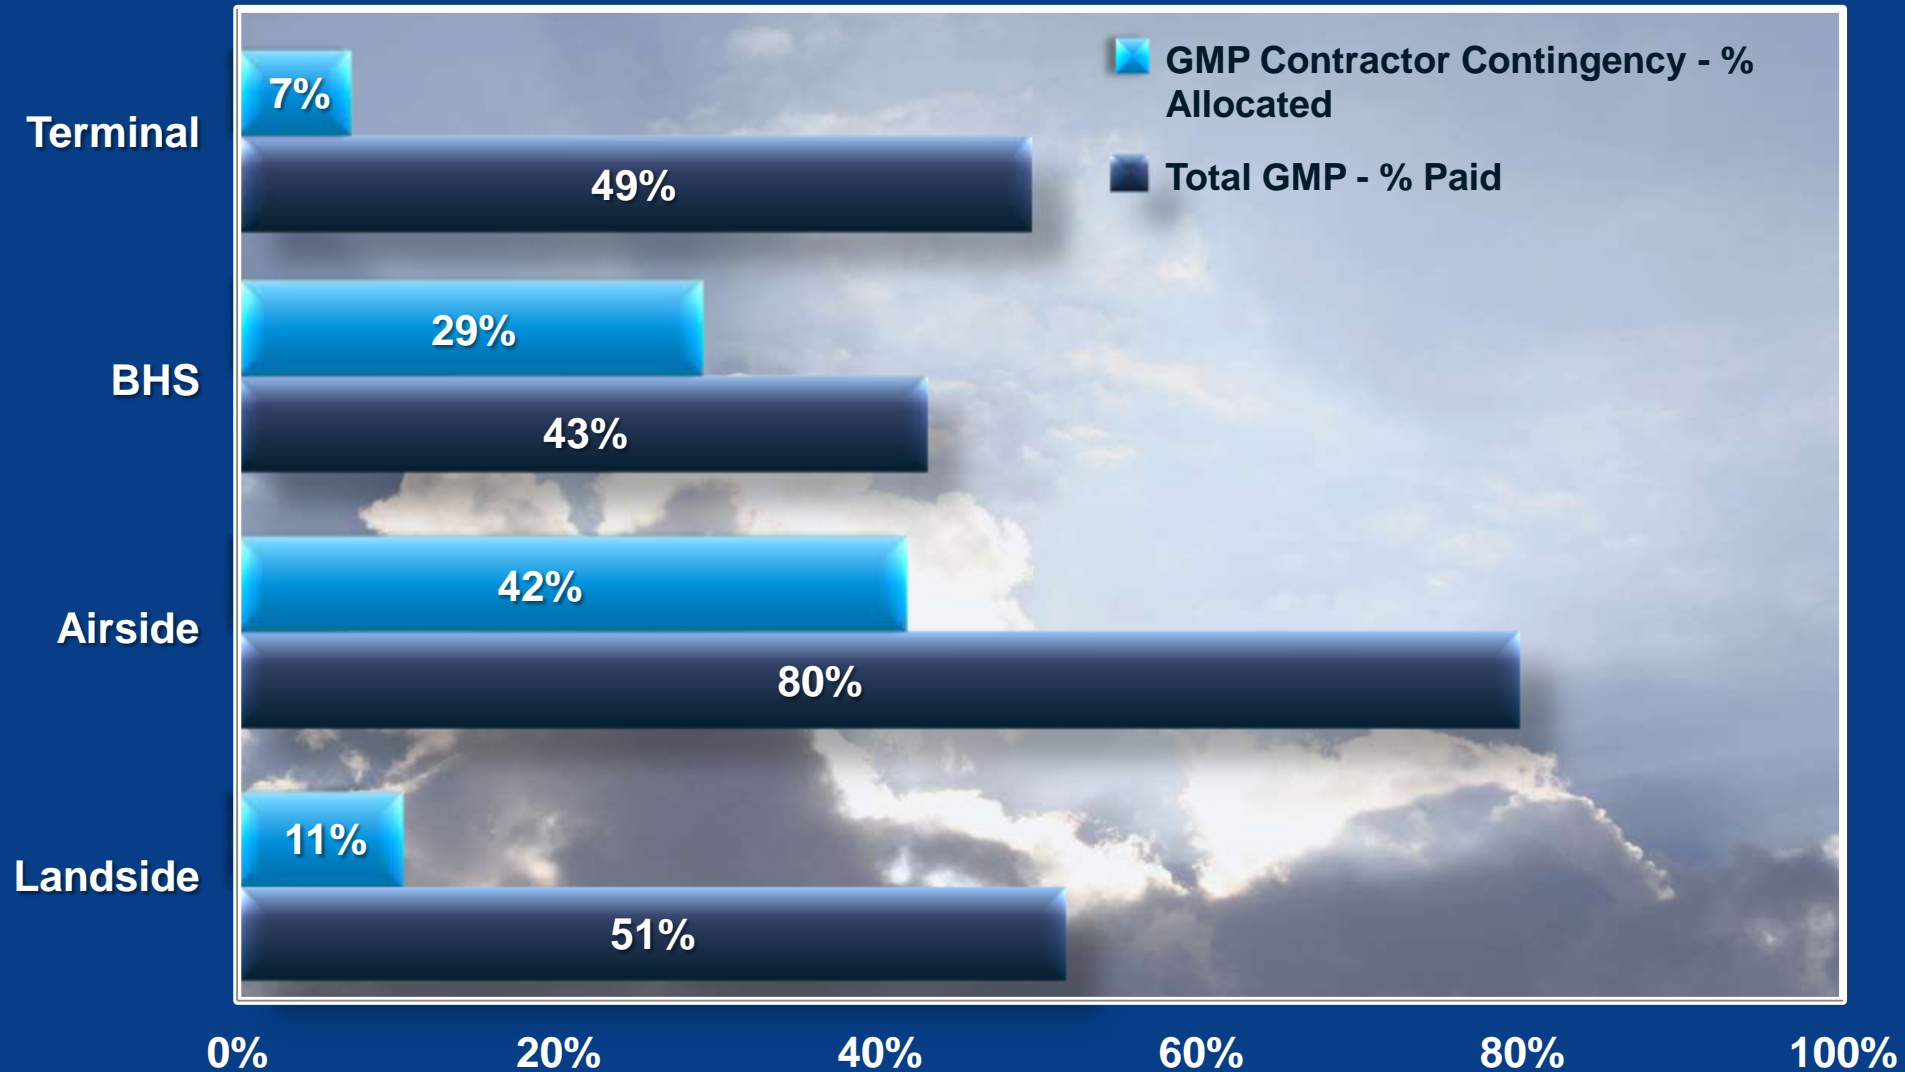

# Questions?

