




Item 2

Green Build Progress Report
Presented by David Brush, Program Director

San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.

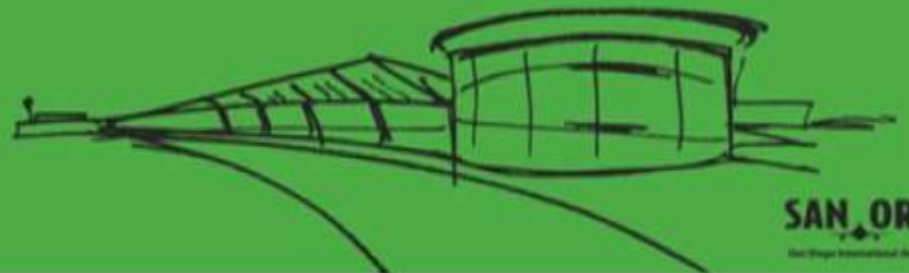

SAN.ORG
San Diego International Airport

Presentation Topics

- Green Build Update
 - Recent Aerial Photos
 - Construction Status
 - Budget Performance

San Diego International Airport


The Green Build


Moving Forward. Soaring Higher.



Green Build Site

September 2012

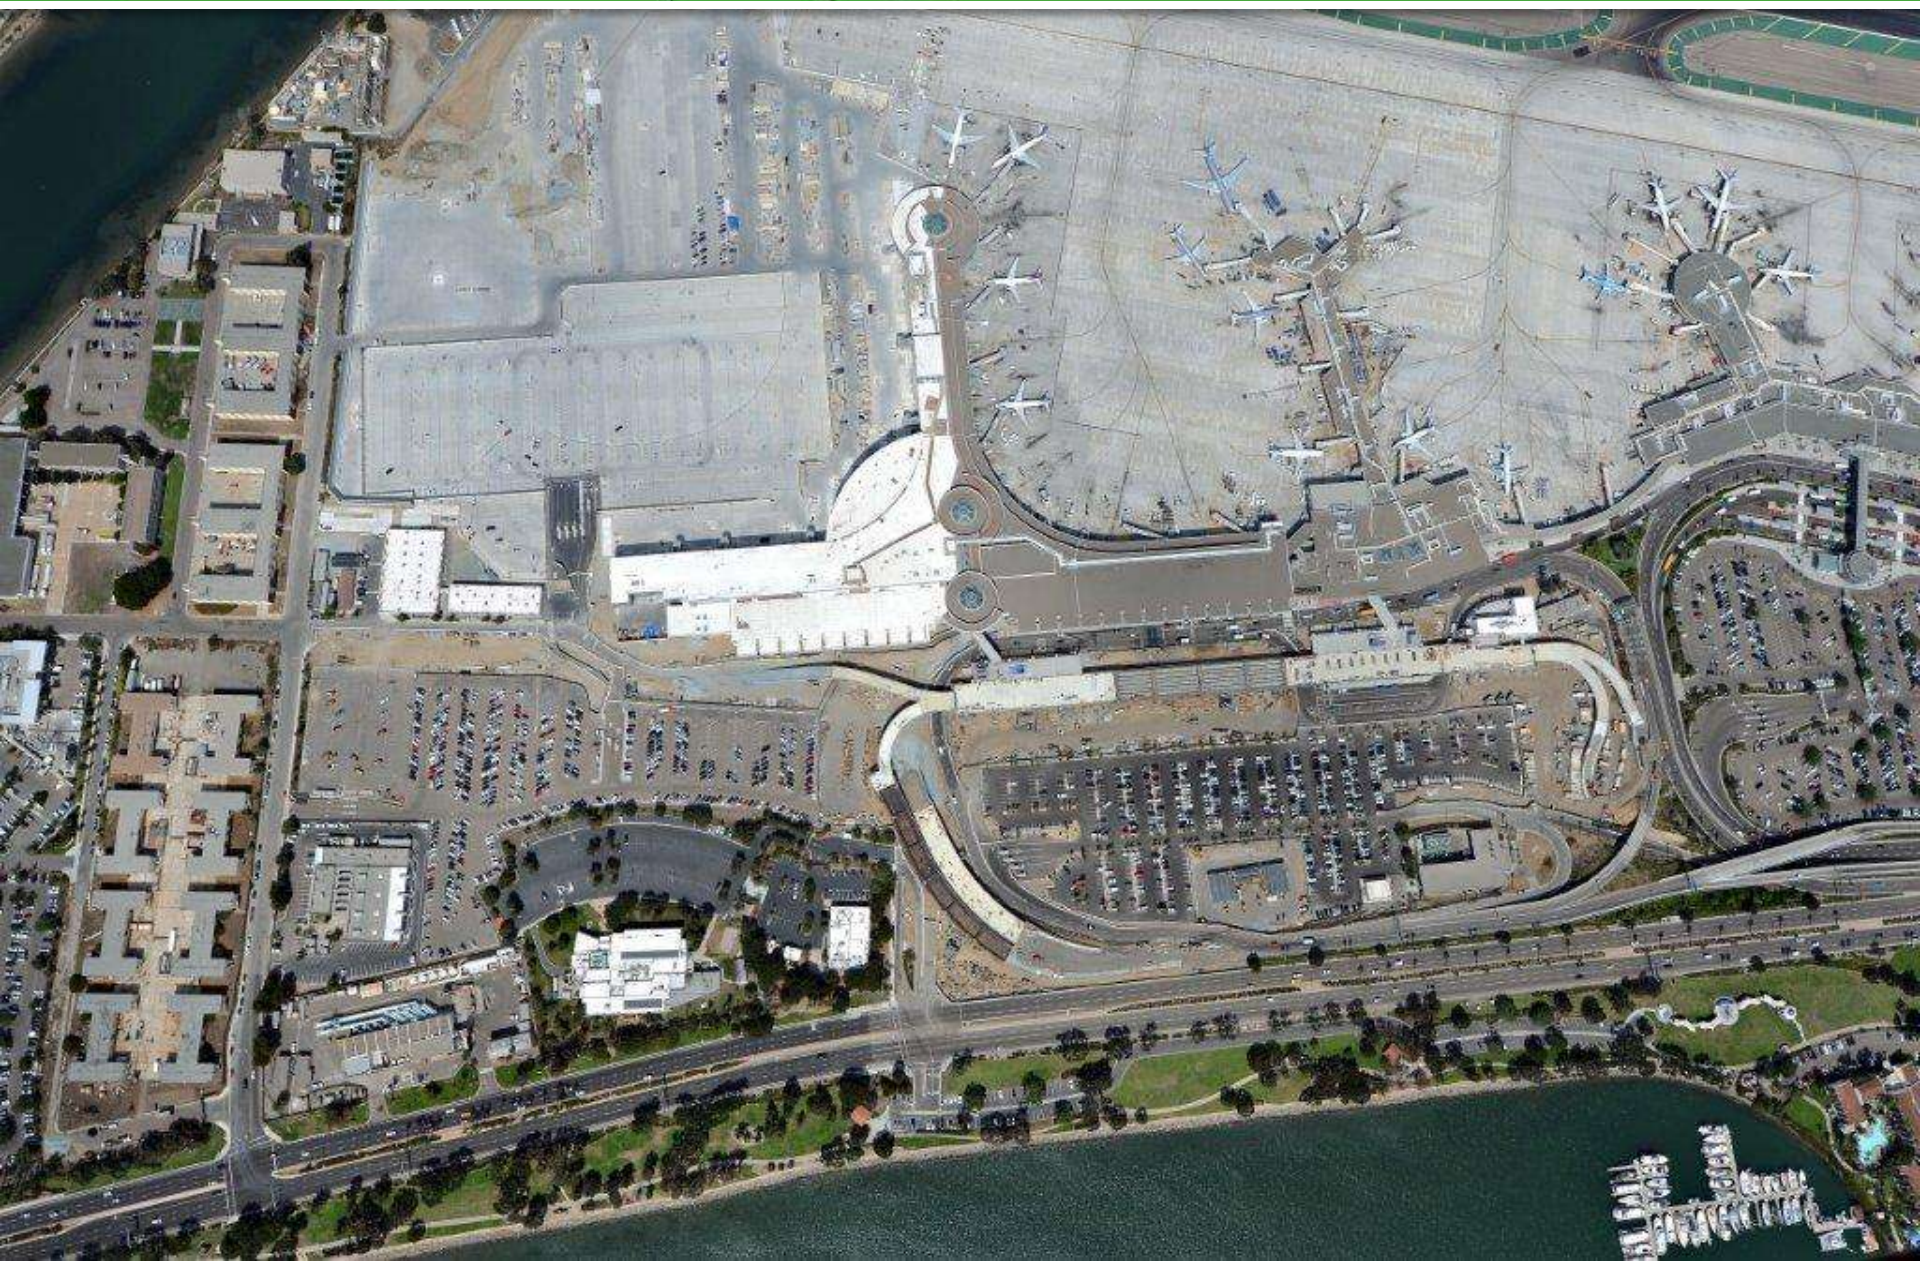



Terminal – Looking North


September 2012



San Diego International Airport


The Green Build

Moving Forward. Soaring Higher.



Terminal – Looking East

September 2012

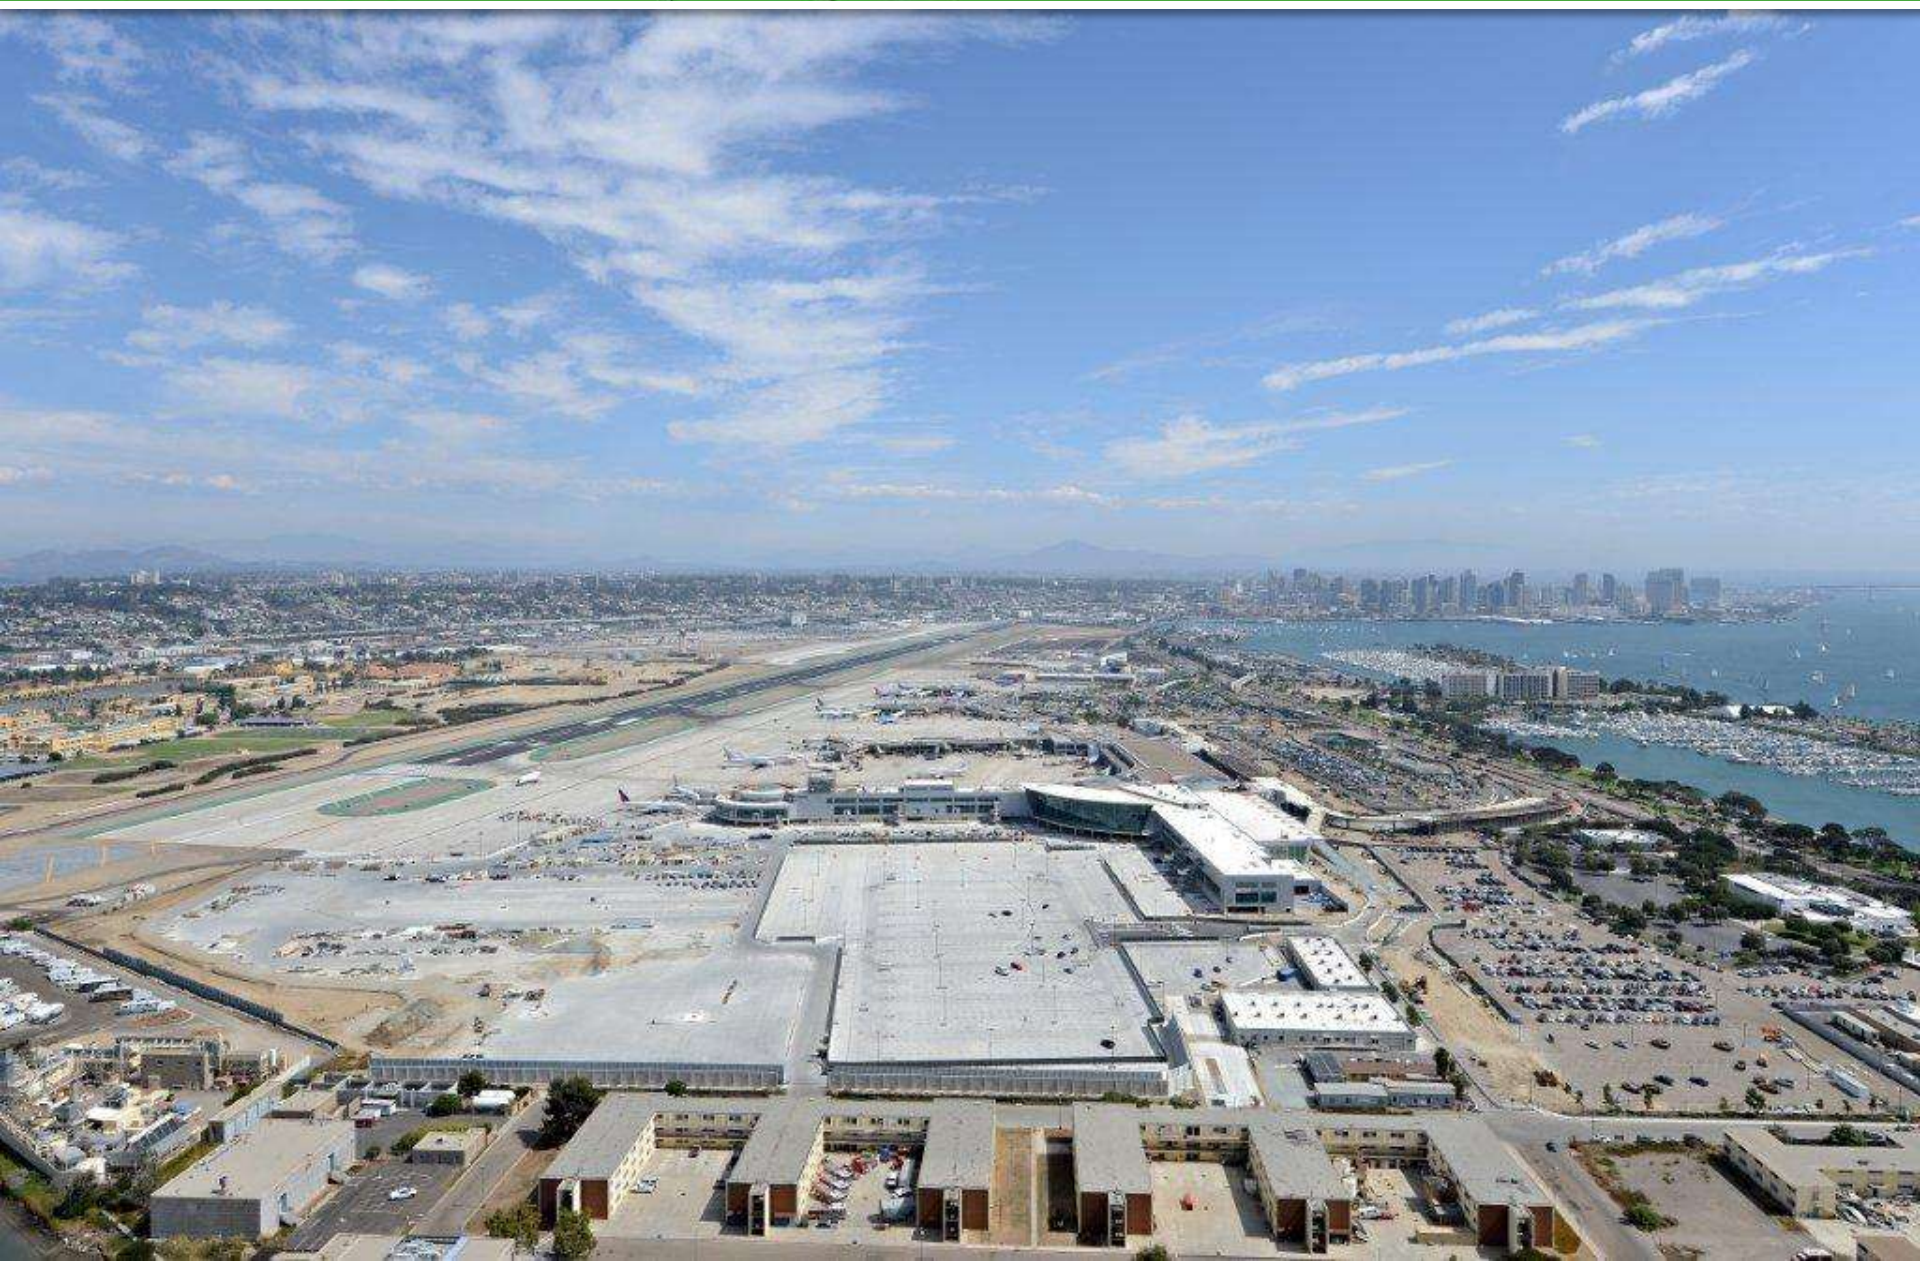

San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.



Sunset Cove


September 2012



San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.




Sunset Cove



San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.



Terrazzo Installation



San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.



Landside

September 2012



San Diego International Airport


The Green Build

Moving Forward. Soaring Higher.



SAN.ORG

Tensile Fabric Structure

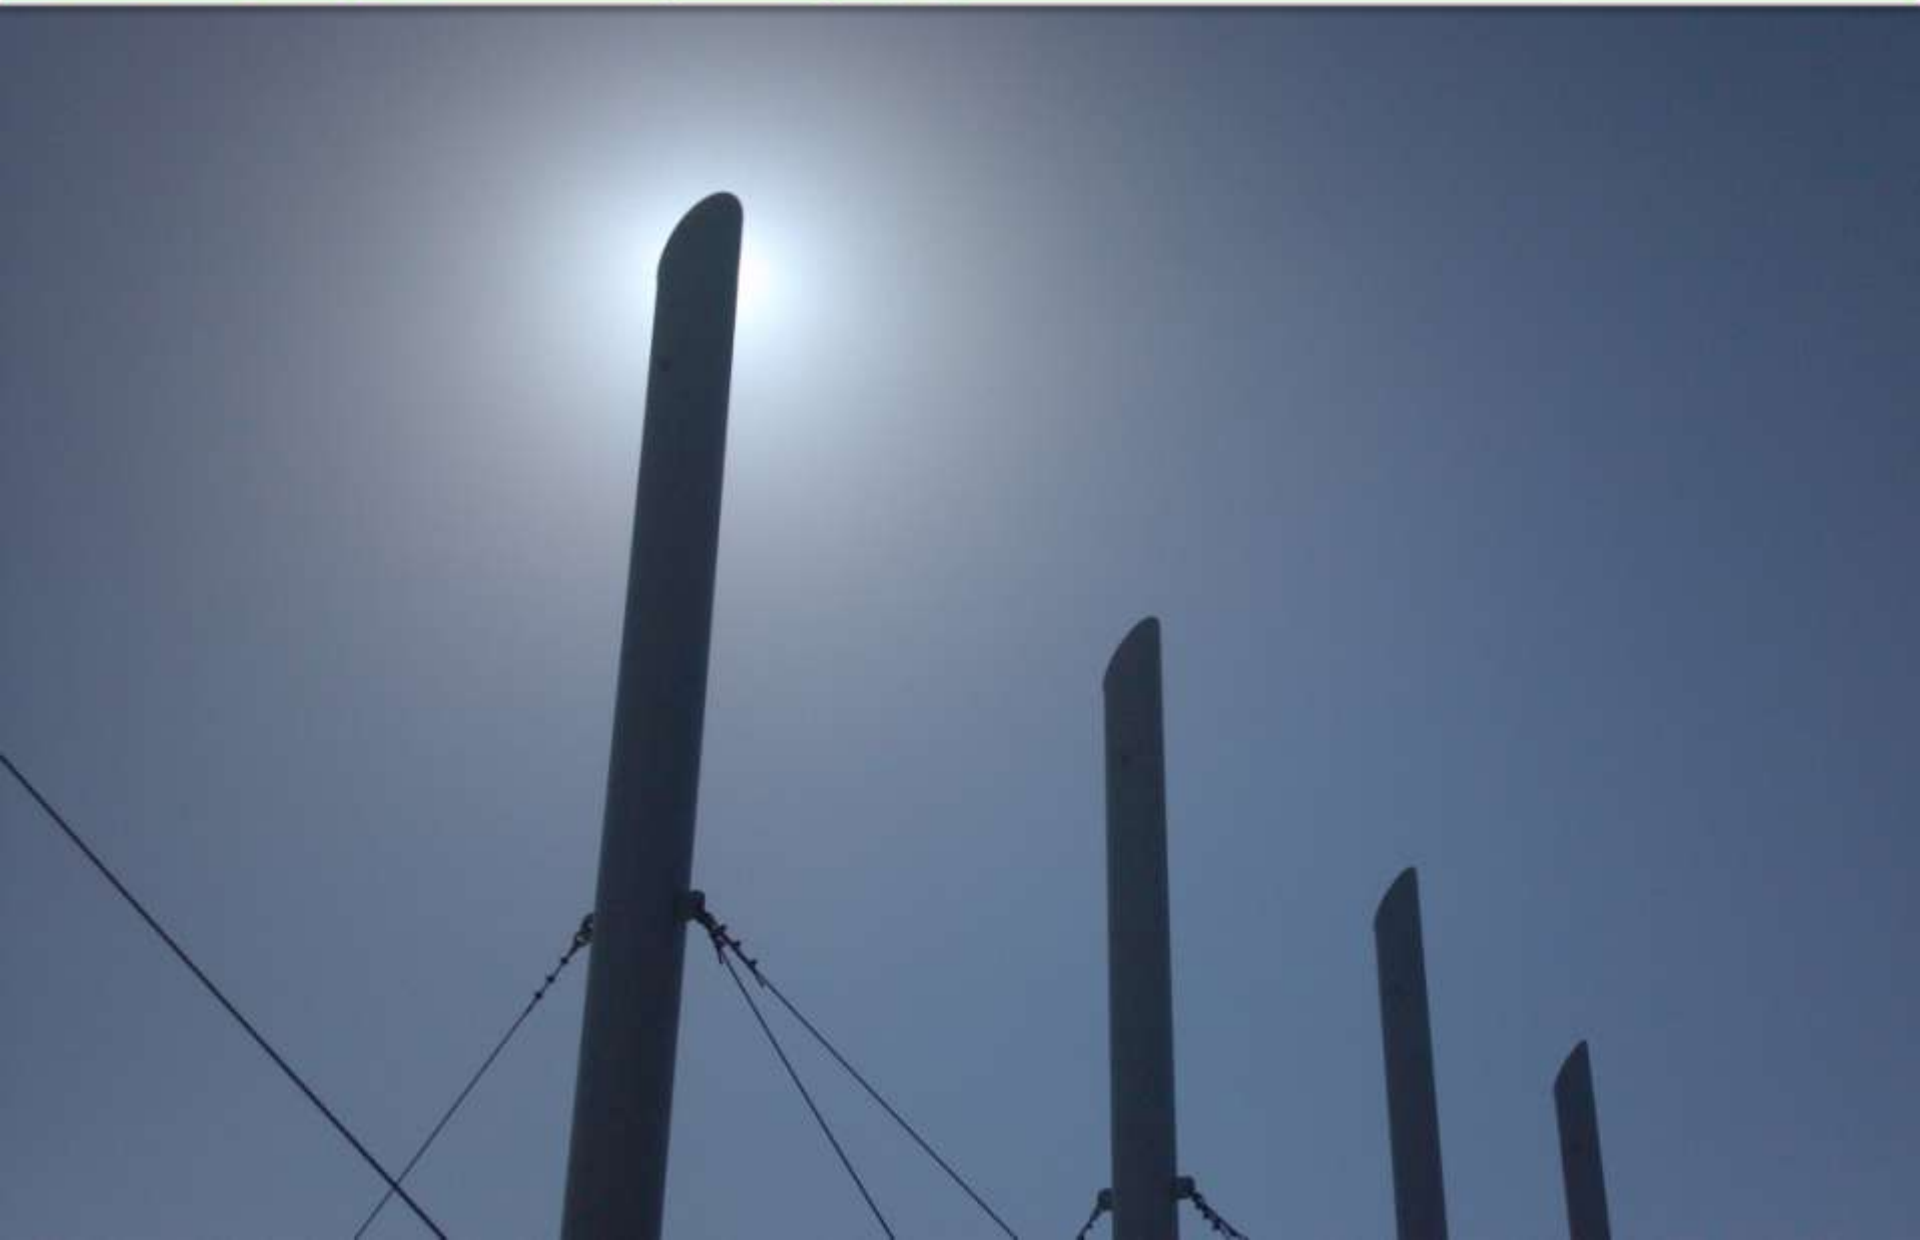

San Diego International Airport

The Green Build
Moving Forward. Soaring Higher.



Tensile Fabric Structure



San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.



SAN.ORG

Tensile Fabric Structure



San Diego International Airport

The Green Build

Moving Forward. Soaring Higher.



USO/PMO
September 2012





Phased Opening Milestones

Event	Planned	Forecast
BHS Go Live	02/25/2013	02/25/2013
Open New Security Screening Check Point	03/22/2013	03/22/2013
Open Six New Gates in North Concourse and Open Apron	04/15/2013	04/15/2013
All T2 Parking Lot Spaces Open	04/29/2013	04/29/2013
Grand Opening	08/2013	08/2013

Questions?

