



## Phased Opening Milestones

Milestone Event	Planned	Forecast
Baggage Handling System	Complete	
Open Security Screening Check Point	Complete	
Open Six New Gates & Aircraft Apron	Complete	
All T2 Parking Lot Spaces Open	Complete	
Grand Opening	08/2013	08/2013

## The Green Build Moving Forward. Soaring Higher.



## **Program Update**



## The Green Build Moving Forward. Soaring Higher.



#### **Check-In Pavilion**



## The Green Build Moving Forward. Soaring Higher.



#### **Check-In Pavilion**









The Green Build
Moving Forward. Soaring Higher.



## USO/PMO


May 2013



## The Green Build Moving Forward. Soaring Higher.




#### **Sunset Cove**

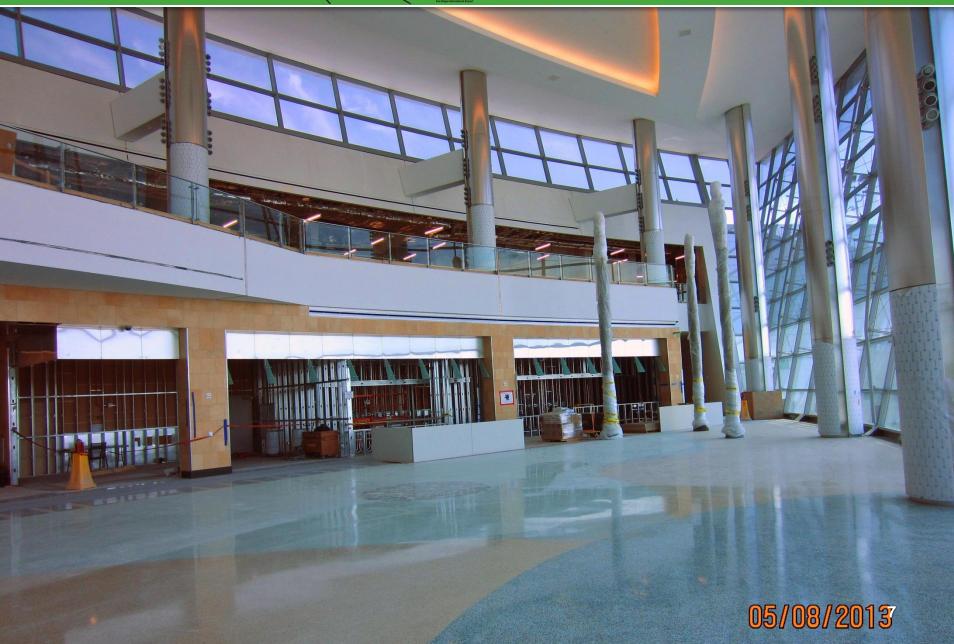

## The Green Build Moving Forward. Soaring Higher.



## **New Ticket Lobby**

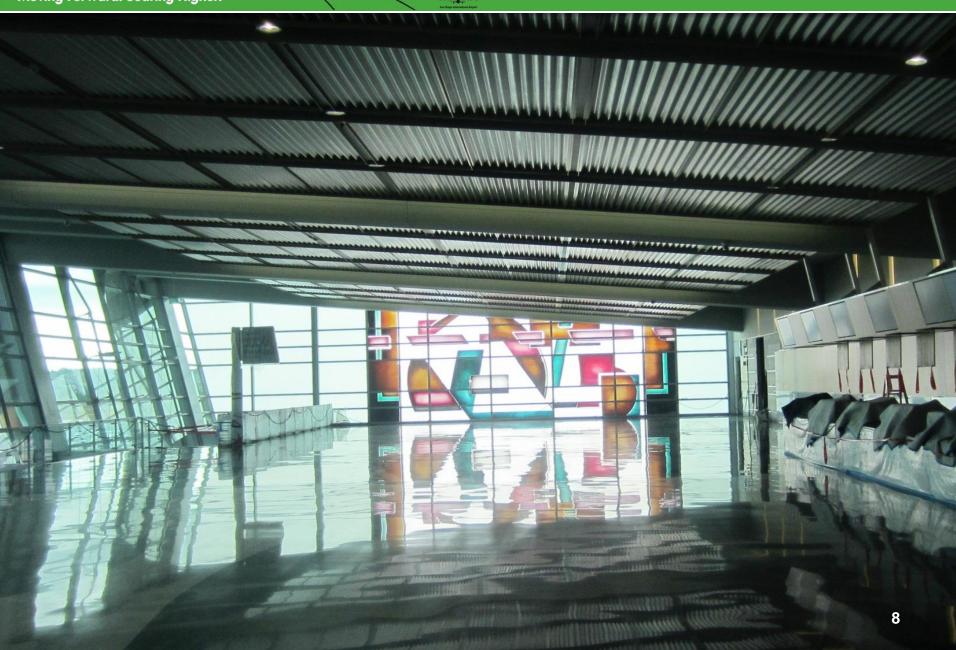

## The Green Build Moving Forward. Soaring Higher.




#### **North Concourse**





### **Canine Security Sweep**

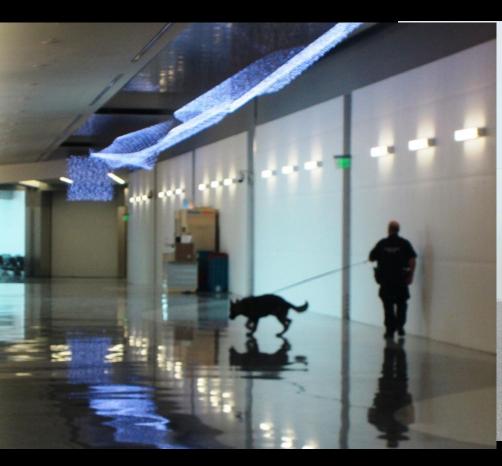




## The Green Build Moving Forward. Soaring Higher.



#### **Final Touches North Concourse**

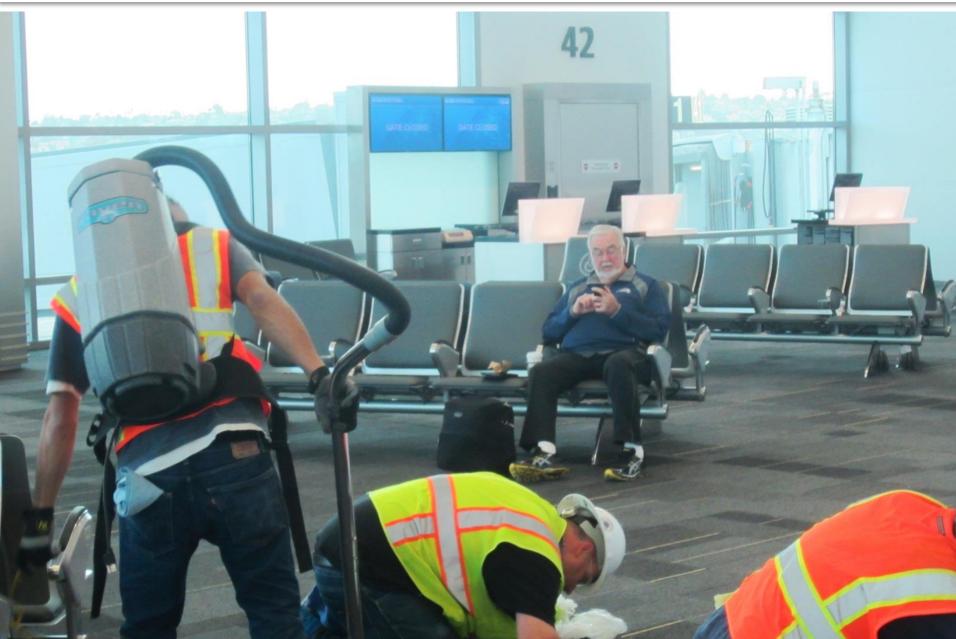

## The Green Build Moving Forward. Soaring Higher.



#### **First Arrival North Concourse**



## The Green Build Moving Forward. Soaring Higher.



#### **Demo of Existing Concourse**

SAN, ORG





#### **LEED Update**



#### Airfield/Terminal (Contract 1)

Current Point Forecast: 42 – Yes; 7 – Maybe

#### Design Submitted on 6/15/12

Submitted – 25

Approved – 25

Rejected - 0

Deferred – 6

Green Building Council Point System

Silver: 33 to 38

Gold: 39 to 51



#### **LEED Update**



#### Landside (Contract 2)

Current Point Forecast 44 – Yes; 0 – Maybe

Design Submitted on 4/30/12

Submitted – 27

Approved – 27

Rejected – 0

Green Building Council Point System


Silver: 33 to 38

Gold: 39 to 51



#### **Budget Status**

Data as of April 30, 2013

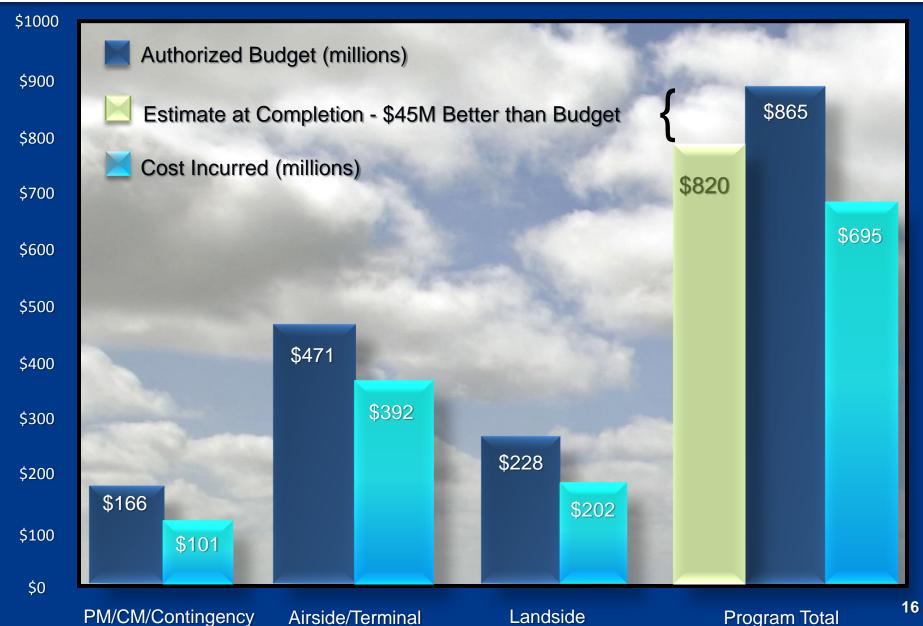

# Questions?

