


January 8, 2013



Green Build Activation Team Update


Murray Bauer
January 22, 2013



January 8, 2013



Green Build Activation Approach

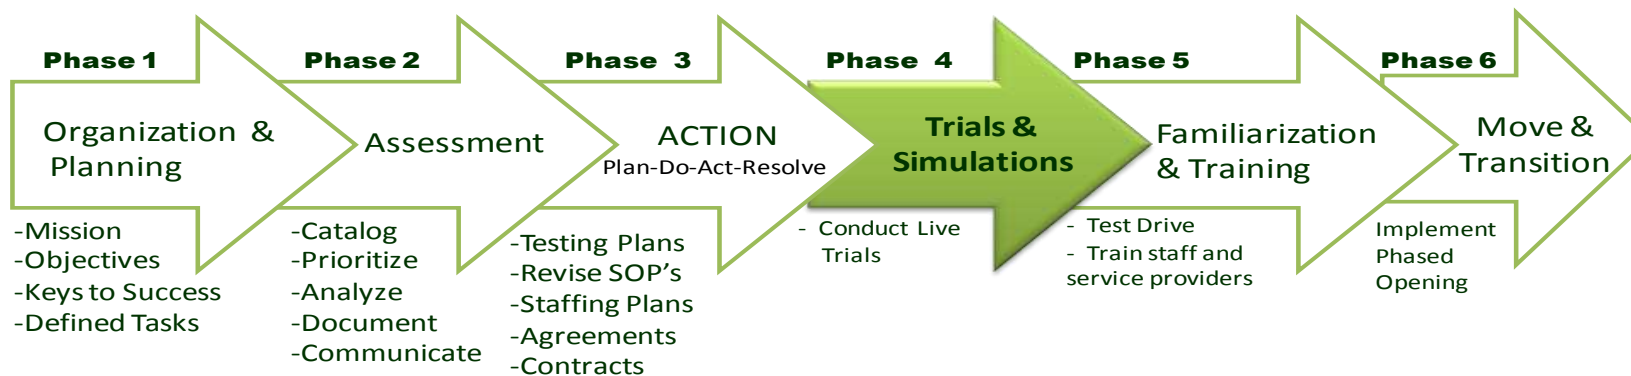


Transit Island Exit Reroute effective 12/12/12



EXHIBIT A - DEC 7, 2012
Kiewit/Sundt - 201401A
Transit Center Exit
DATE: 12/11/12
TIME: 11 pm






PMO

(Parking Management Office)

PMO schedule to open on January 22, 2013



CUPPS

(Common Use Passenger Processing System)

T2E testing is complete and operational as of Nov 15th.

Carriers currently using the CUPPS platform are:

American Airlines

British Airlines

Hawaiian Airlines


Japan Airlines

Jet Blue

US Air

Volaris

WestJet




CUSS (Common Use Self Service)

Testing of the Green Build approved KIOSK's are in the planning stages for live testing.

KIOSK's will be located on the first floor of T2E.


Testing of the elevated departure curb skycap systems are in the planning stages with American Airlines.

PHASE I Level 1

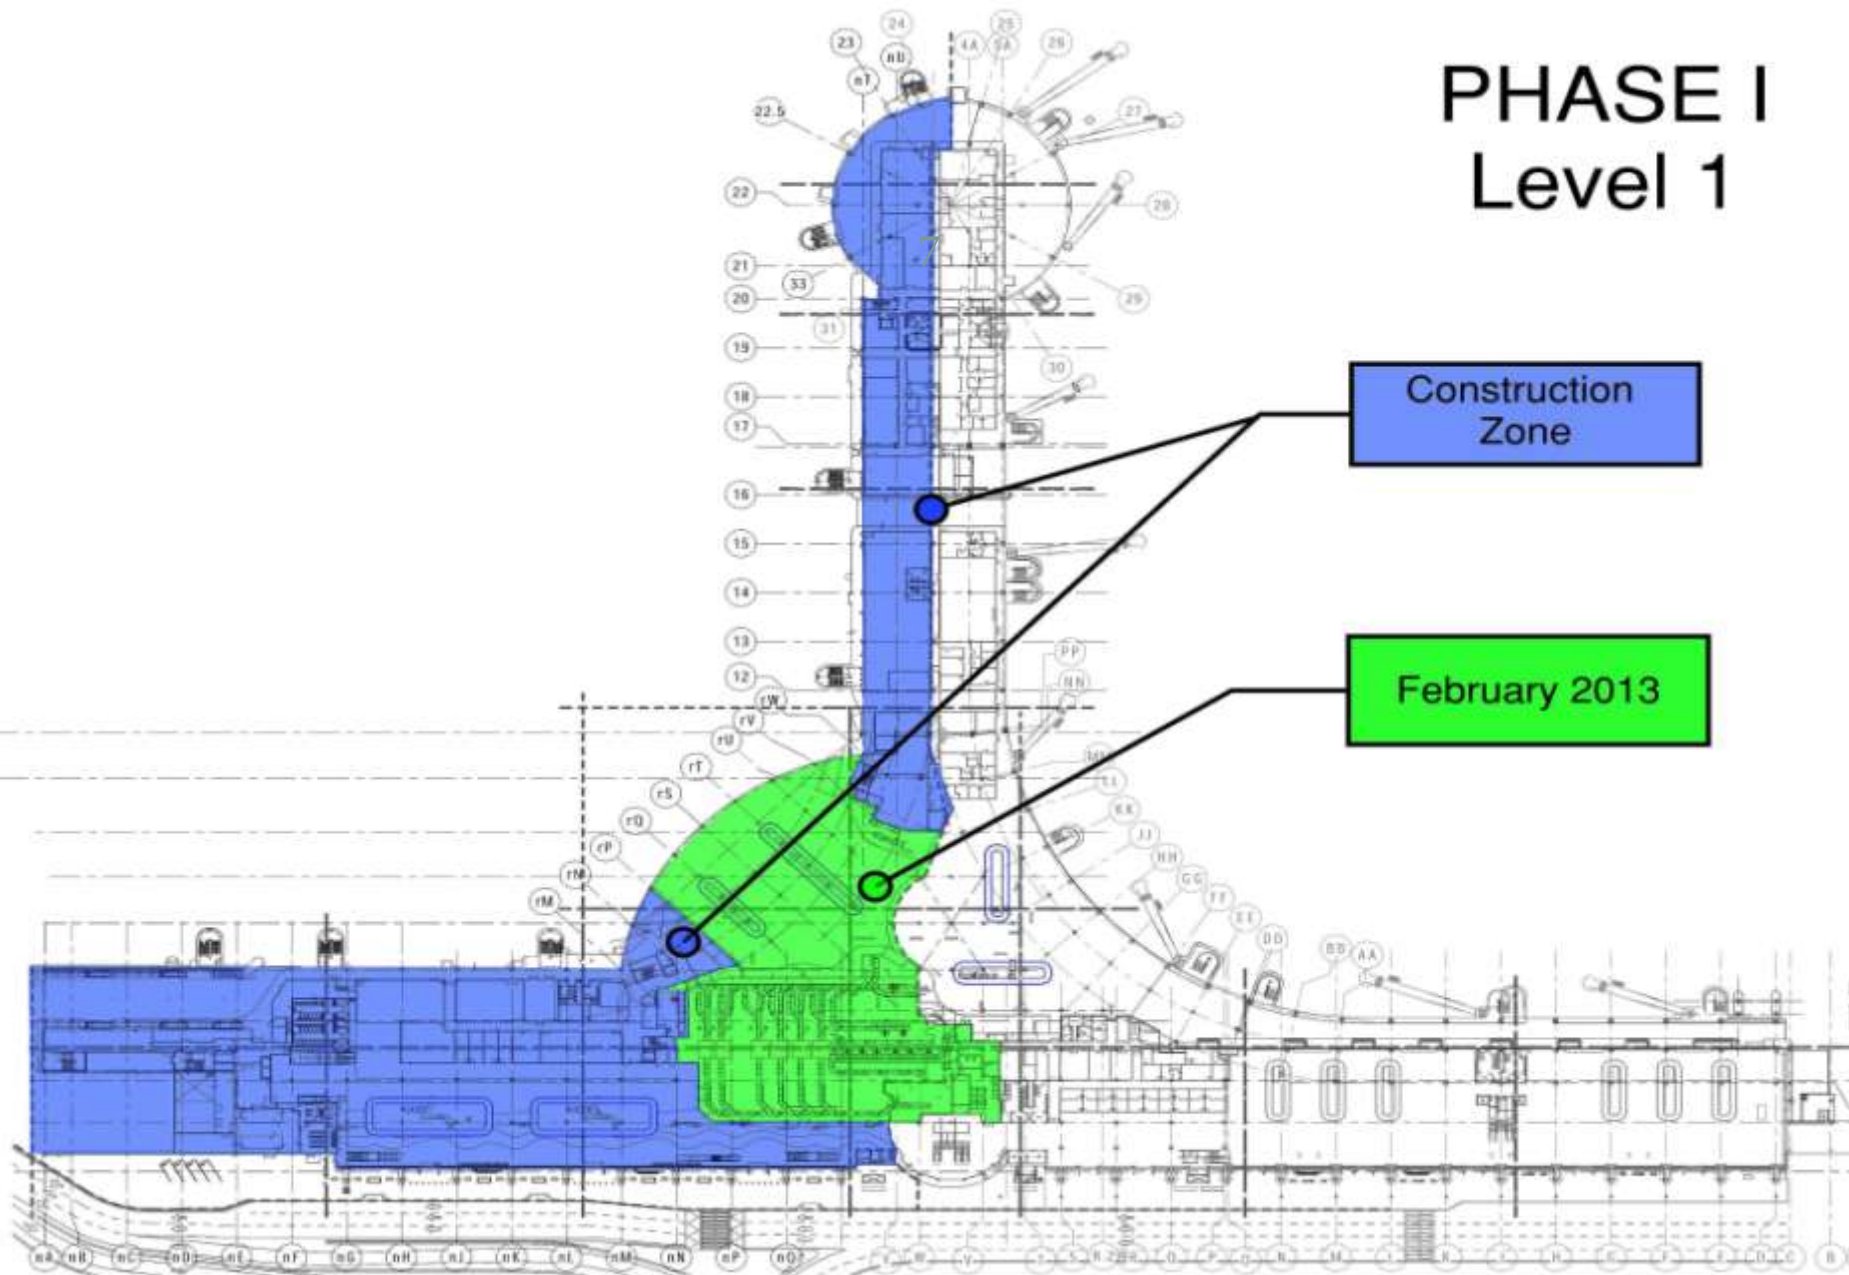


New Outbound Baggage Screening & Sortation

PHASE II Level 2

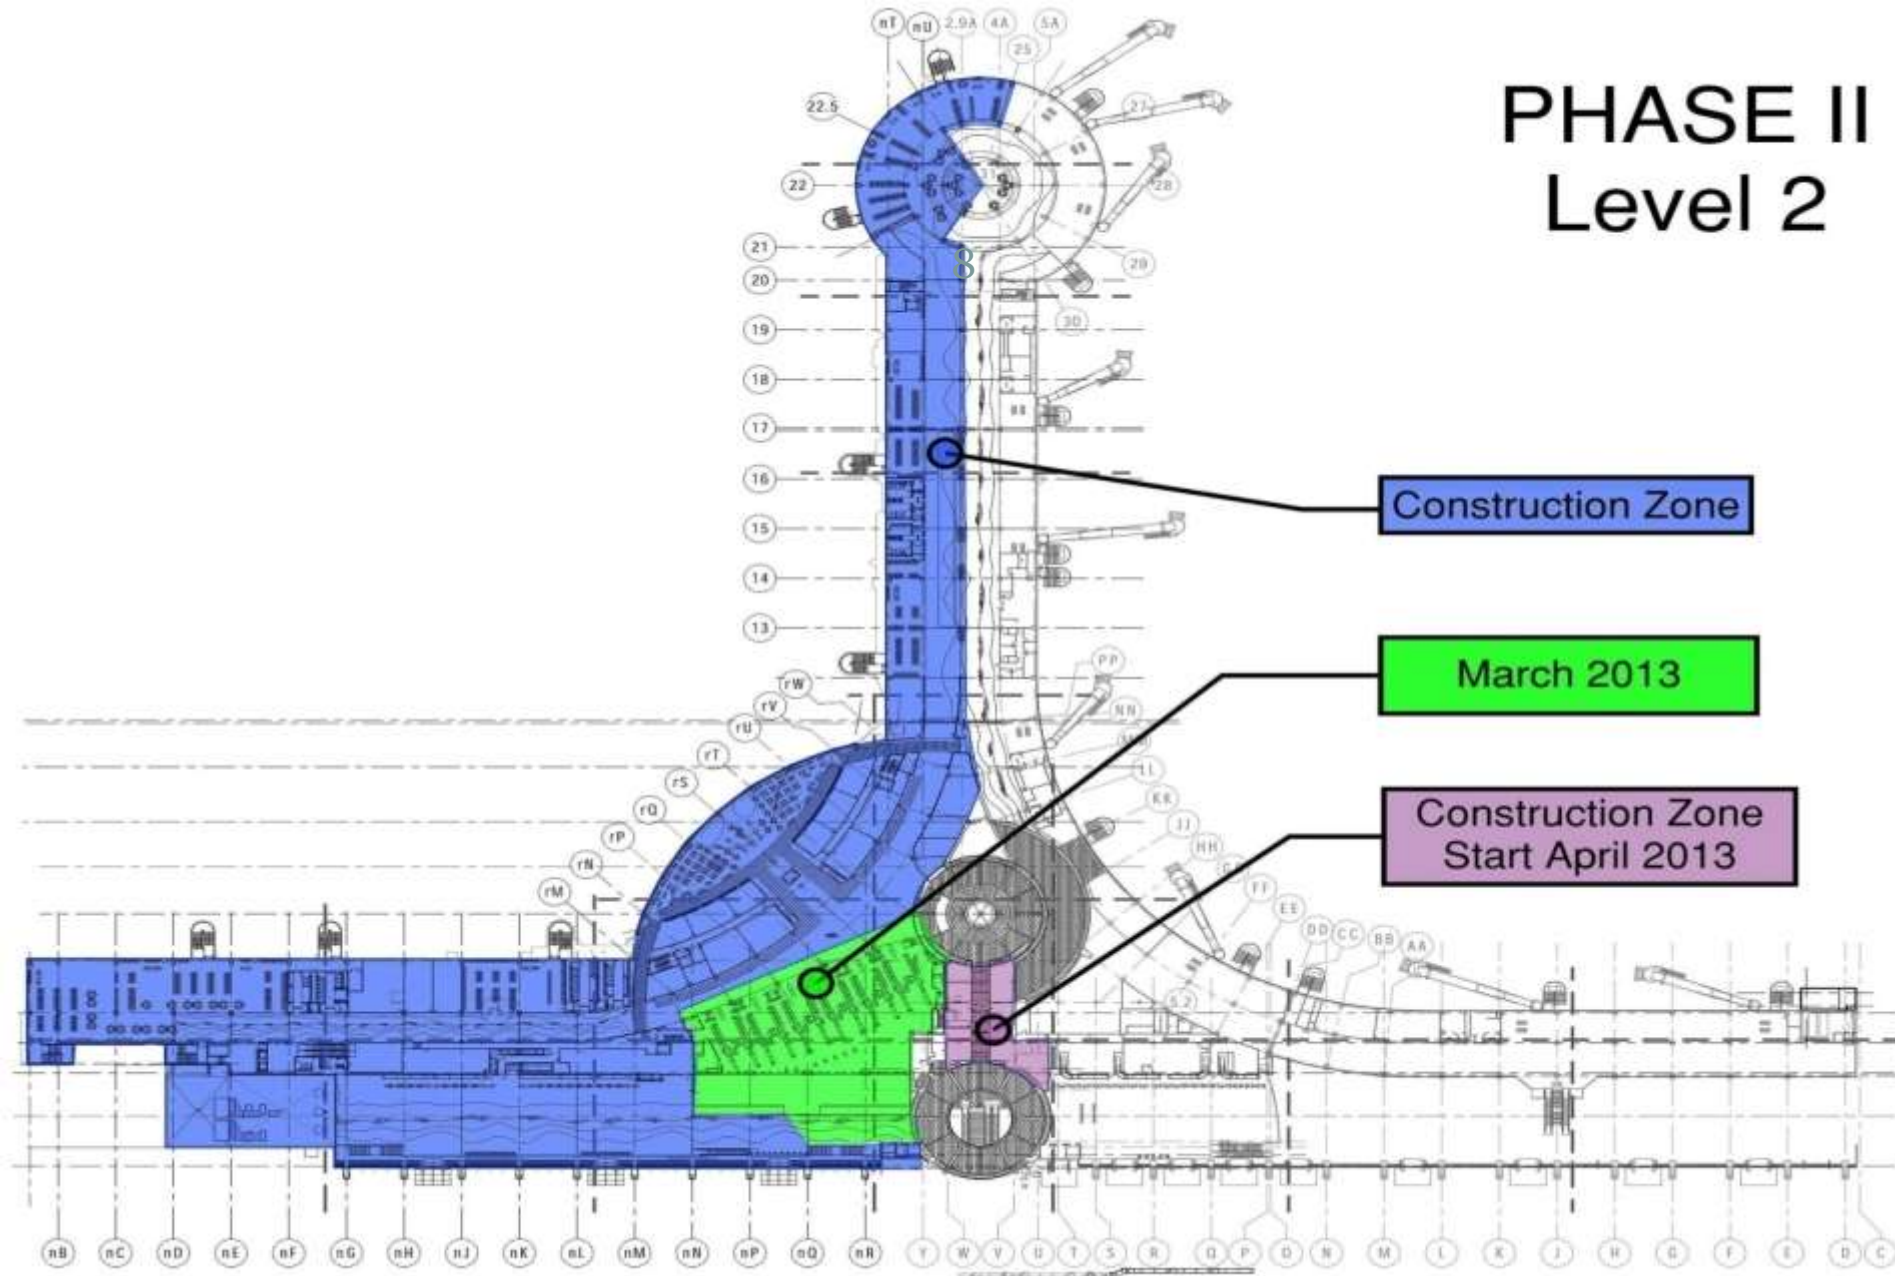


New Security Checkpoint

PHASE III Level 2

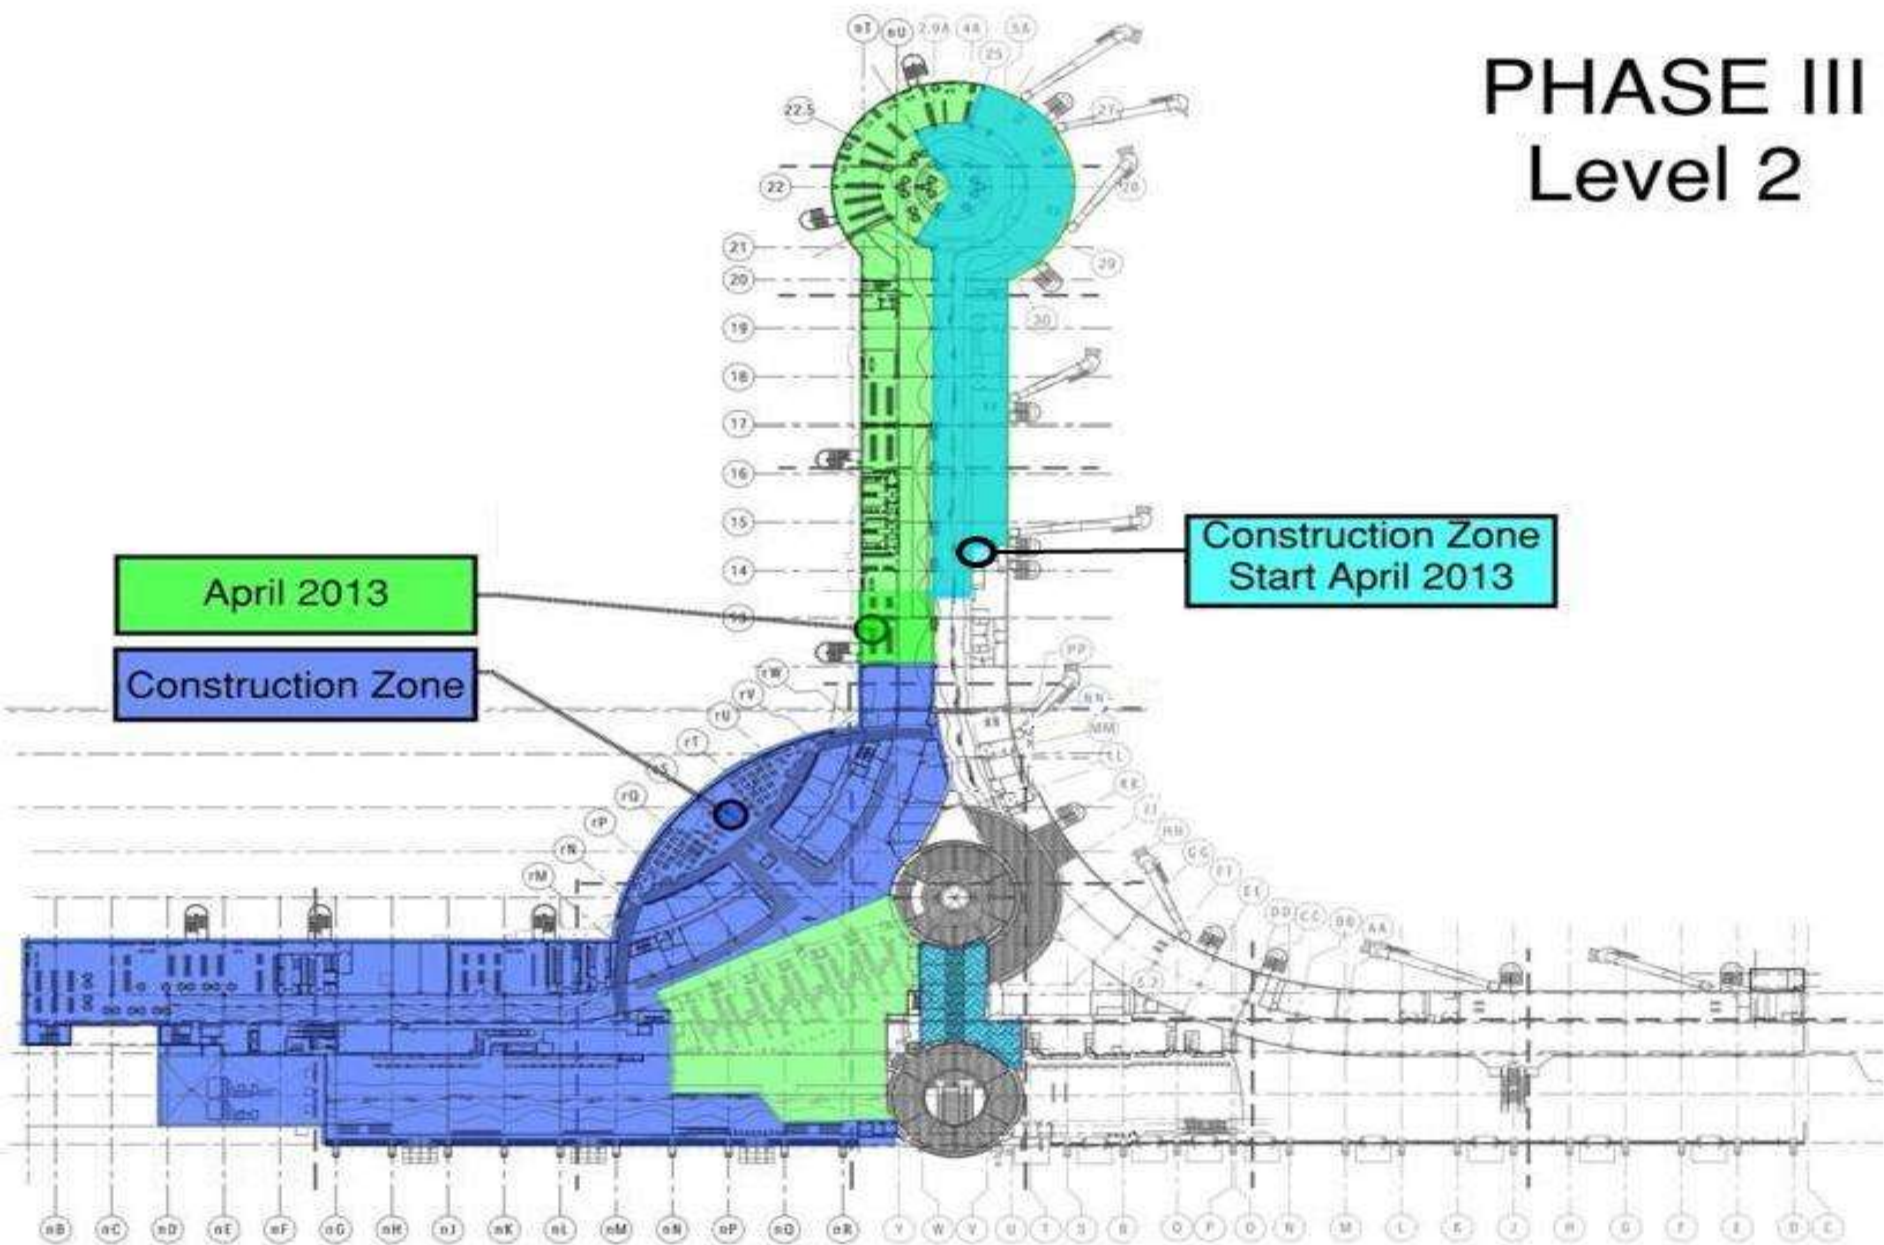

Close 37-41 Gates/Open 42-47 Gates



January 8, 2013



Questions
